SOFTWARE ENGINEERING LAB 2

Agile Project Planning and Sprint Simulation using Jira

Alumni Mentorship & Mock Interview Platform

Student: Akash Ramesh
SRN: PES1UG24AM212
Problem Statement: Alumni Mentorship & Mock Interview Platform
Jira Project: Alumni Mentorship & Mock Interview Platform
Jira Project Key: SCRUM
Sprints: SCRUM Sprint 1 and SCRUM Sprint 2

A. Epic and User Story Table

The table below lists the Epics created for the Alumni Mentorship & Mock Interview Platform and the User Stories associated with each Epic. The table also records the story points, priority and sprint allocation used during the Jira sprint simulation.

Epic	Epic Key	User Story	Issue Key	Story Points	Priority	Sprint
Mentor Discovery & Matching	SCRUM-6	Search Alumni Mentors	SCRUM-11	3	High	Sprint 1
Mentor Discovery & Matching	SCRUM-6	Match Student with Mentor	SCRUM-12	5	Highest	Sprint 1
Session Booking & Scheduling	SCRUM-7	View Mentor Availability	SCRUM-13	3	High	Sprint 1

Session Booking & Scheduling	SCRUM-7	Book Mentorship Session	SCRUM-14	5	Highest	Sprint 1
Mentor Availability Management	SCRUM-8	Define Mentor Availability	SCRUM-15	3	High	Sprint 1
Platform Performance & Security	SCRUM-10	Protect User Information	SCRUM-16	5	High	Sprint 1
Session Booking & Scheduling	SCRUM-7	Synchronize Session with Calendar	SCRUM-17	3	High	Sprint 2
Mentorship & Mock Interview	SCRUM-9	Join Video Mentorship Session	SCRUM-18	3	High	Sprint 2
Mentorship & Mock Interview	SCRUM-9	Conduct Mock Interview	SCRUM-19	5	High	Sprint 2
Mentorship & Mock Interview	SCRUM-9	Submit Post-Interview Scorecard	SCRUM-20	5	High	Sprint 2
Mentor Availability Management	SCRUM-8	Block Unavailable Time Slots	SCRUM-21	3	High	Sprint 2
Platform Performance & Security	SCRUM-10	Ensure Quick Platform Response	SCRUM-22	3	Medium	Sprint 2
Total	**5 Epics**	**12 User Stories**		**46**		

B. Evaluation Criteria and Evidence

Evaluation Criterion	Evidence in this Document
Create Epics and User Stories	Epic and User Story Table; Epic screenshot; User Story screenshots
Assign Story Points / Planning Poker	Story Point and Planning Poker section; Story Points column in the table
Prioritize and Rank Backlog	Priority and Backlog Ranking section; Jira backlog screenshot
Run Sprint 1	Sprint 1 creation, sprint board, progress and comments screenshots
Run Sprint 2	Sprint 2 creation, sprint board, progress and comments screenshots
Generate Burndown Chart	Sprint 1 and Sprint 2 Burndown Chart screenshots
Sprint Summary	Sprint 1 and Sprint 2 summary screenshots
Reflection	Group/Individual Reflection section

1. Epics and User Stories

Five Epics were created for the Alumni Mentorship & Mock Interview Platform. These Epics divide the system into major functional areas: mentor discovery and matching, session booking and scheduling, mentor availability management, mentorship and mock interviews, and platform performance and security.

Twelve User Stories were created and associated with the appropriate Epics. Each User Story represents a specific requirement from the perspective of a user of the platform.

The five Epics are:

1. **Mentor Discovery & Matching**
2. **Session Booking & Scheduling**
3. **Mentor Availability Management**
4. **Mentorship & Mock Interview**
5. **Platform Performance & Security**

Figure 1 – Epics created in Jira

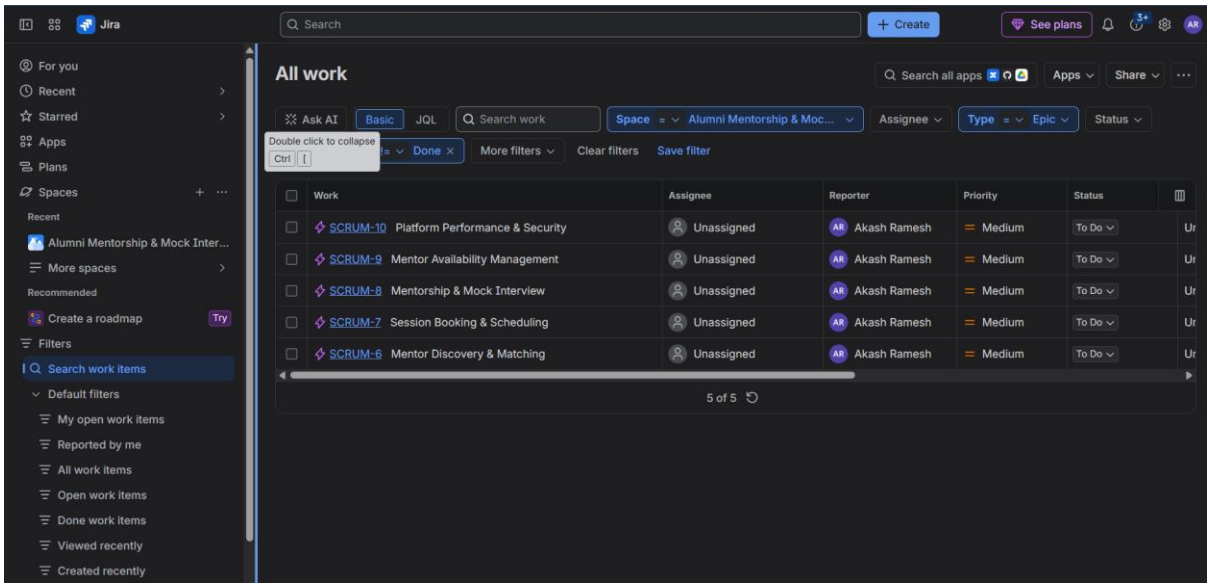
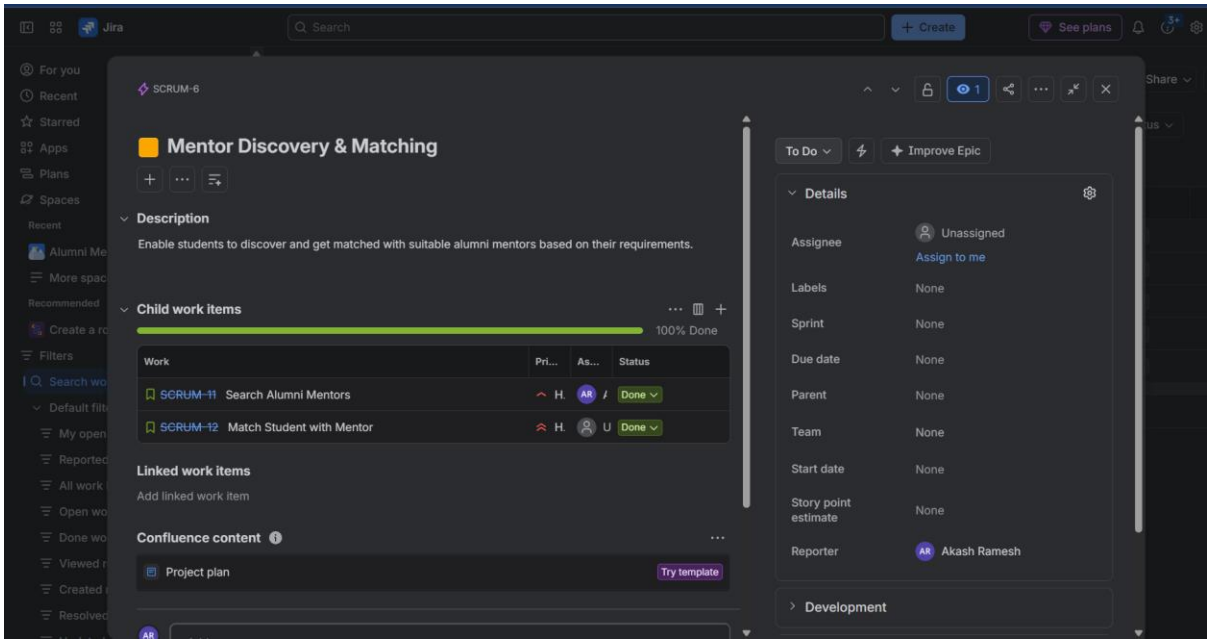
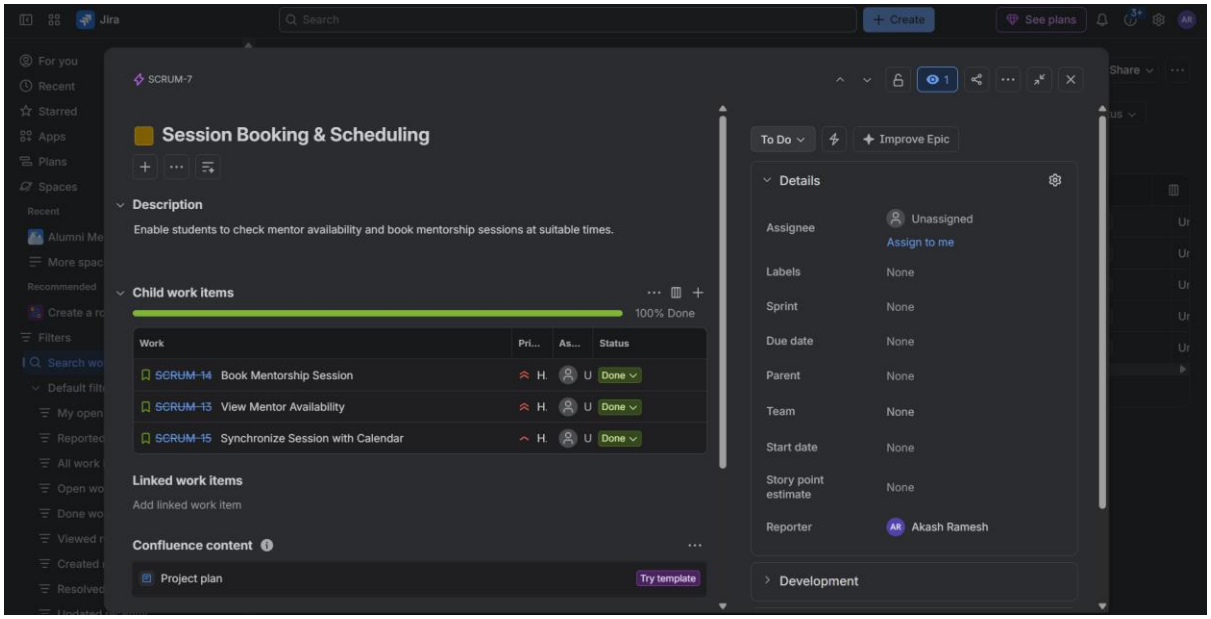
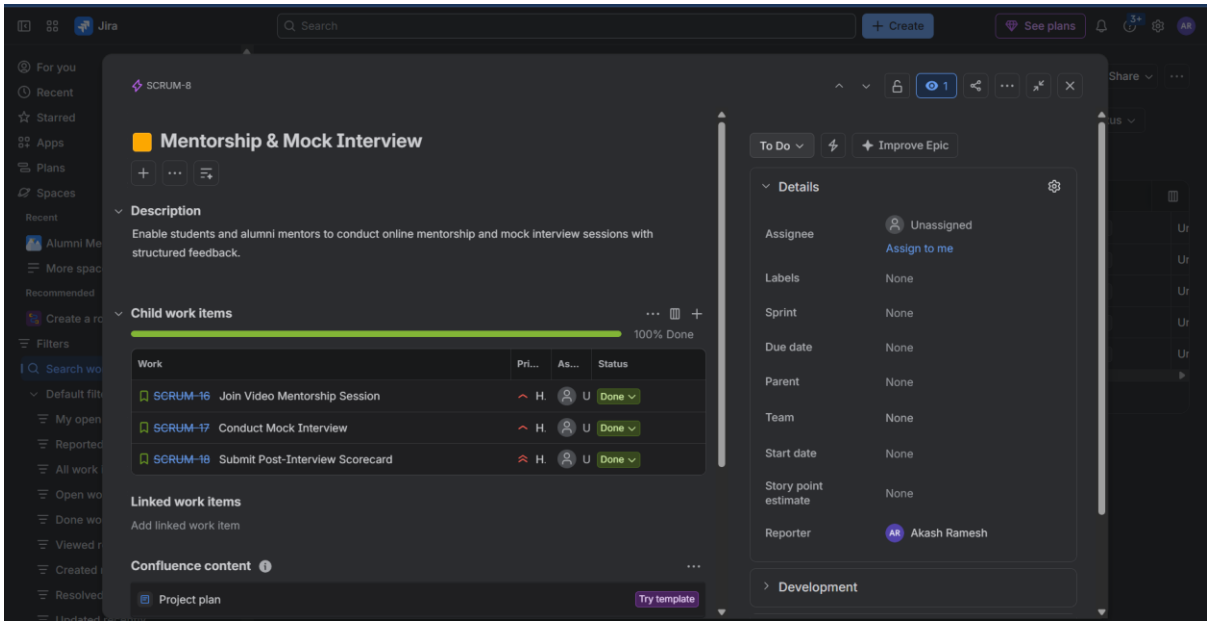
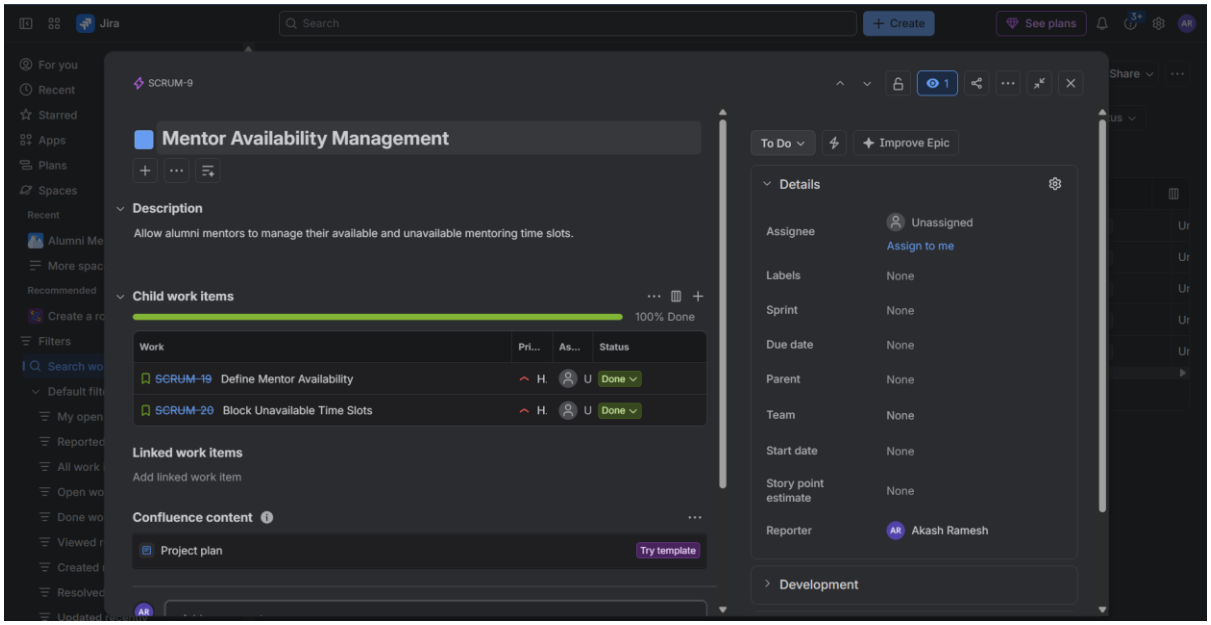


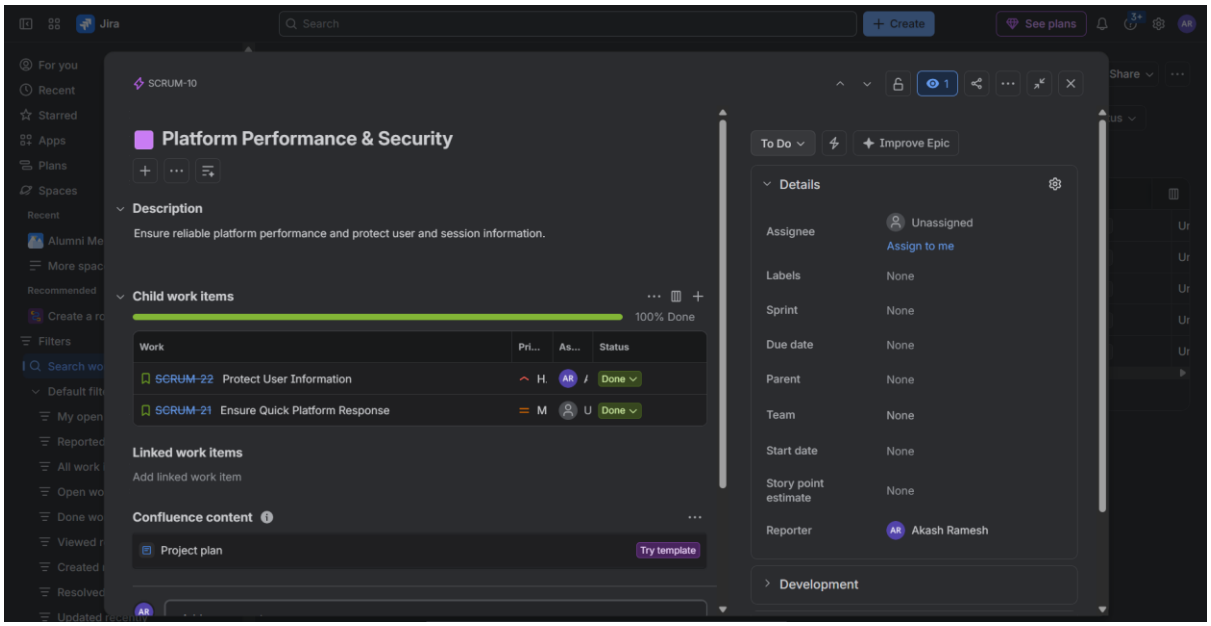
Figure 2 – User Stories created in Jira


Jira
Search
Create
See plans
SCRUM-6
Mentor Discovery & Matching
Description
Enable students to discover and get matched with suitable alumni mentors based on their requirements.
Child work items
100% Done
Work
Pri...
As...
Status
SCRUM-11 Search Alumni Mentors
H.
Done
SCRUM-12 Match Student with Mentor
H.
U
Done
Linked work items
Add linked work item
Confluence content
Project plan
Try template
To Do
Improve Epic
Details
Assignee
Unassigned
Assign to me
Labels
None
Sprint
None
Due date
None
Parent
None
Team
None
Start date
None
Story point estimate
None
Reporter
Akash Ramesh
Development


Jira
Search
Create
See plans
SCRUM-7
Session Booking & Scheduling
Description
Enable students to check mentor availability and book mentorship sessions at suitable times.
Child work items
100% Done
Work
Pri...
As...
Status
SCRUM-14 Book Mentorship Session
H.
U
Done
SCRUM-13 View Mentor Availability
H.
U
Done
SCRUM-15 Synchronize Session with Calendar
H.
U
Done
Linked work items
Add linked work item
Confluence content
Project plan
Try template
To Do
Improve Epic
Details
Assignee
Unassigned
Assign to me
Labels
None
Sprint
None
Due date
None
Parent
None
Team
None
Start date
None
Story point estimate
None
Reporter
Akash Ramesh
Development


SCRUM-8
Mentorship & Mock Interview
Description
Enable students and alumni mentors to conduct online mentorship and mock interview sessions with structured feedback.
Child work items
100% Done
Work
Pri...
As...
Status
SCRUM-16 Join Video Mentorship Session
SCRUM-17 Conduct Mock Interview
SCRUM-18 Submit Post-Interview Scorecard
Linked work items
Add linked work item
Confluence content
Project plan
Try template
To Do
Improve Epic
Details
Assignee
Unassigned
Assign to me
Labels
None
Sprint
None
Due date
None
Parent
None
Team
None
Start date
None
Story point estimate
None
Reporter
Akash Ramesh
Development


SCRUM-9
Mentor Availability Management
Description
Allow alumni mentors to manage their available and unavailable mentoring time slots.
Child work items
100% Done
Work
Pri...
As...
Status
SCRUM-19 Define Mentor Availability
SCRUM-20 Block Unavailable Time Slots
Linked work items
Add linked work item
Confluence content
Project plan
Try template
To Do
Improve Epic
Details
Assignee
Unassigned
Assign to me
Labels
None
Sprint
None
Due date
None
Parent
None
Team
None
Start date
None
Story point estimate
None
Reporter
Akash Ramesh
Development


SCRUM-10
Platform Performance & Security
Description
Ensure reliable platform performance and protect user and session information.
Child work items
100% Done
Work
Pri...
As...
Status
SCRUM-22 Protect User Information
SCRUM-21 Ensure Quick Platform Response
Linked work items
Add linked work item
Confluence content
Project plan
Try template
To Do
Improve Epic
Details
Assignee
Unassigned
Assign to me
Labels
None
Sprint
None
Due date
None
Parent
None
Team
None
Start date
None
Story point estimate
None
Reporter
Akash Ramesh
Development

2. Story Points and Planning Poker Estimation

Planning Poker

Story points were used to estimate the relative effort and complexity of the User Stories in the Alumni Mentorship & Mock Interview Platform.

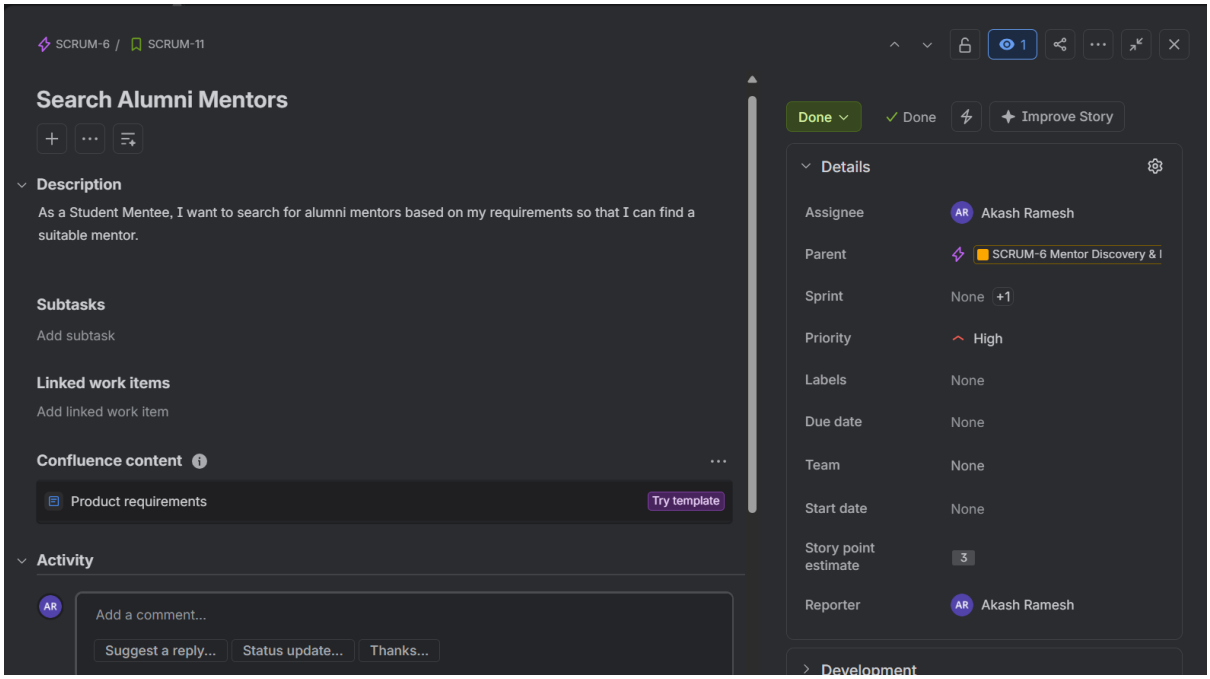
Planning Poker uses a Fibonacci-style sequence such as **1, 2, 3, 5 and 8**. Team members independently estimate the complexity of a User Story and then discuss differences between the estimates before agreeing on a final value.

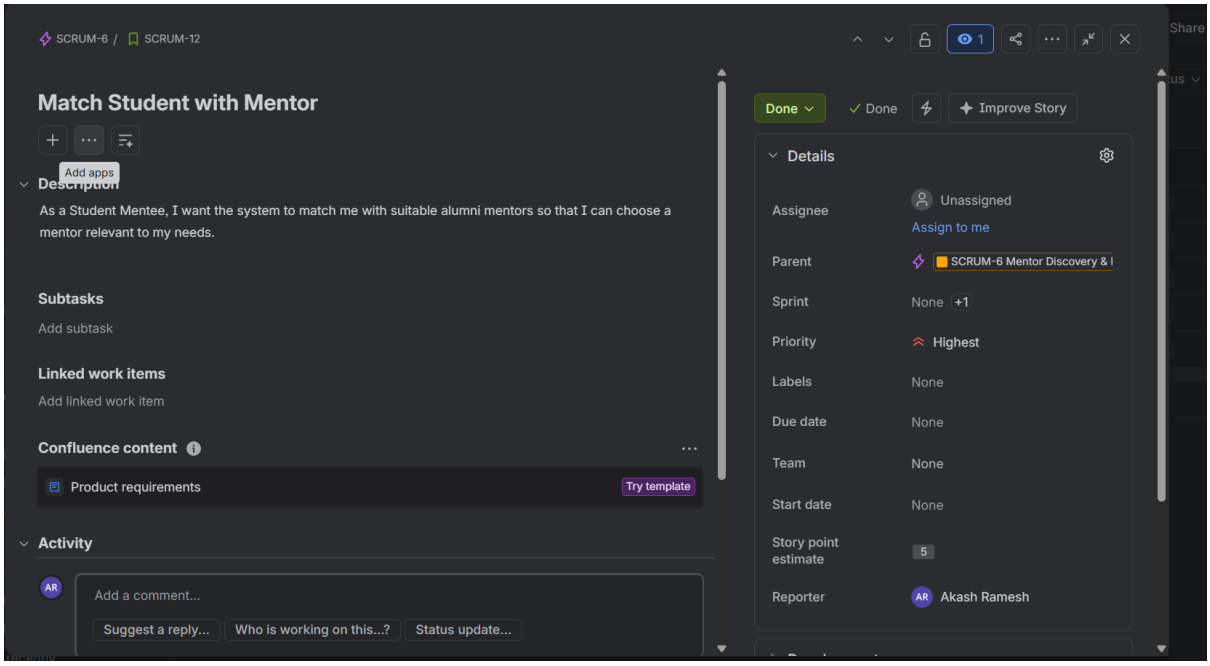
For this project, the User Stories were assigned Fibonacci-based story points. The estimates represent relative effort rather than a direct measurement of time.

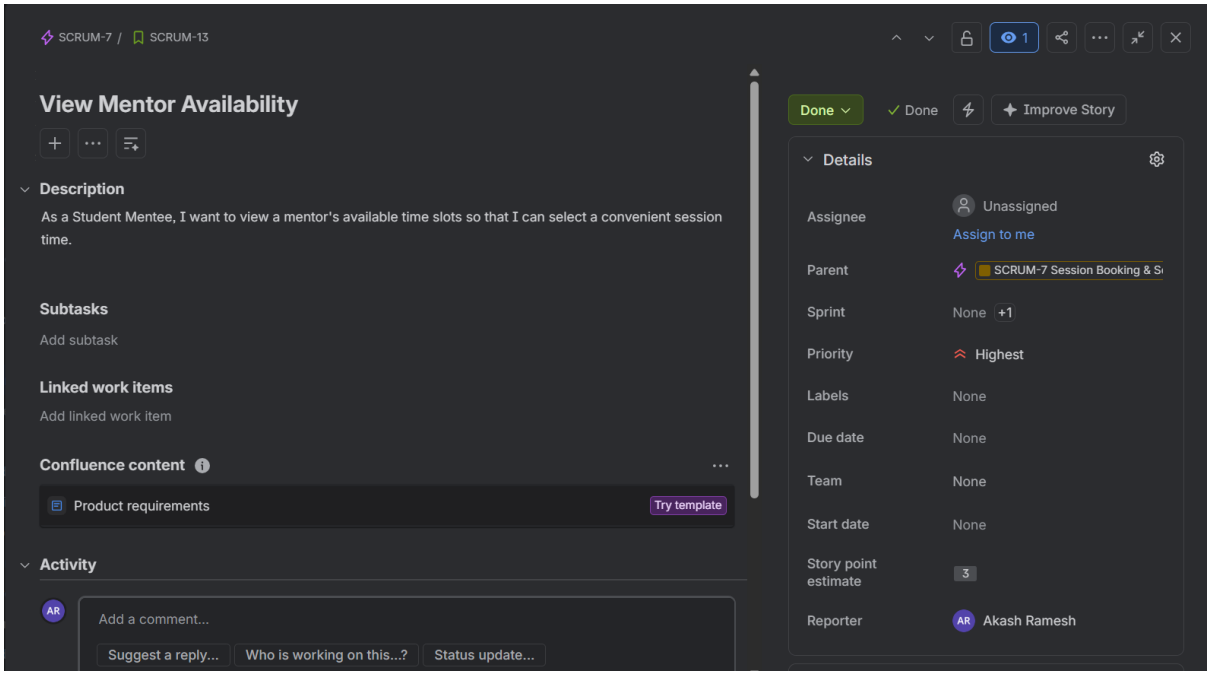
The agreed estimates were recorded in Jira and used during sprint planning.

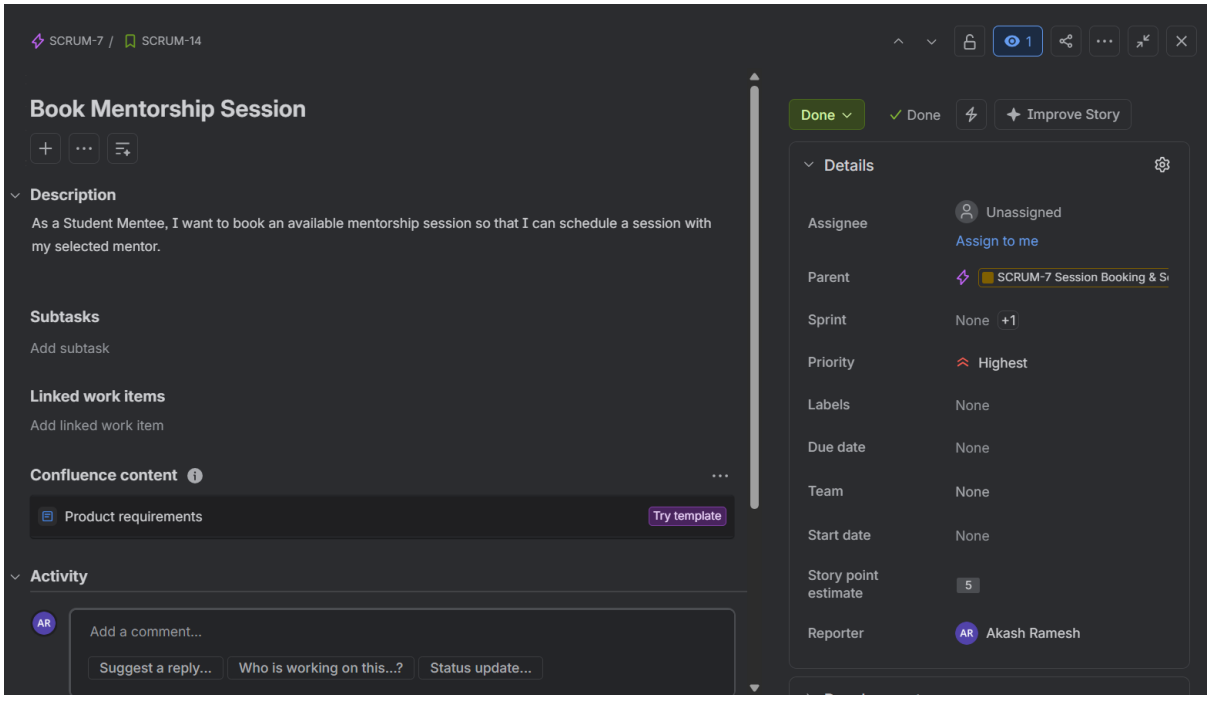
Story Points	Number of Stories	Total Points
3	7	21
5	5	25
Total	**12**	**46**

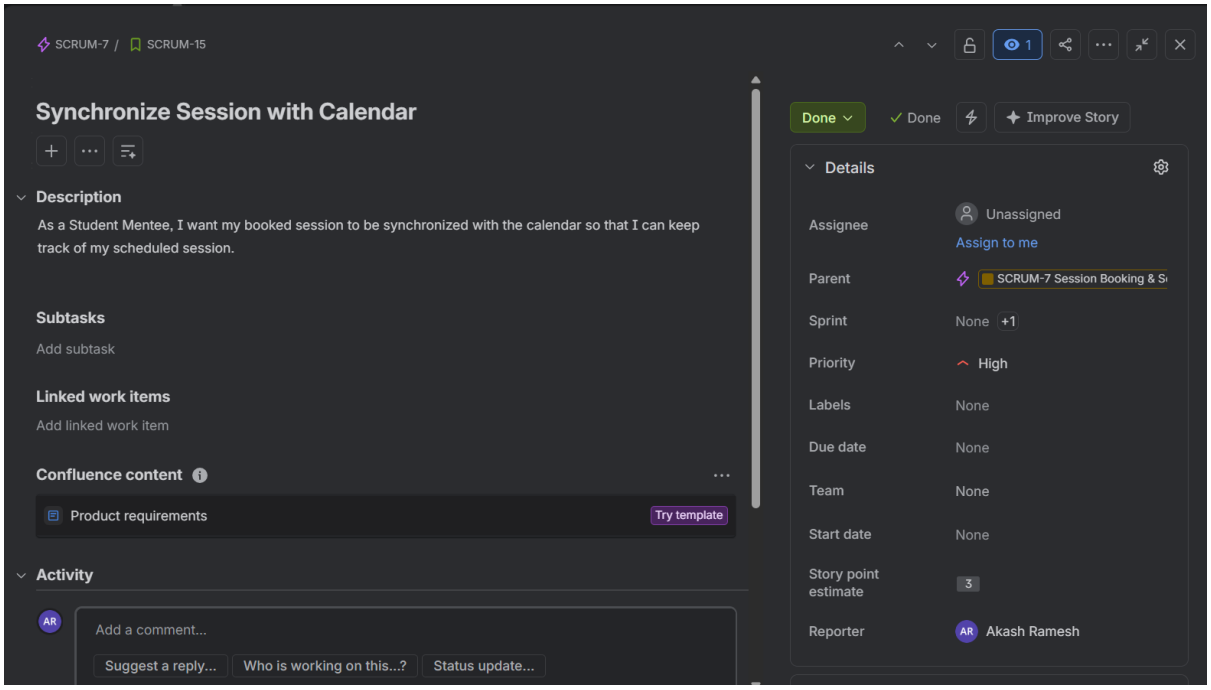
The story-point estimates helped determine which User Stories could be committed to each sprint.

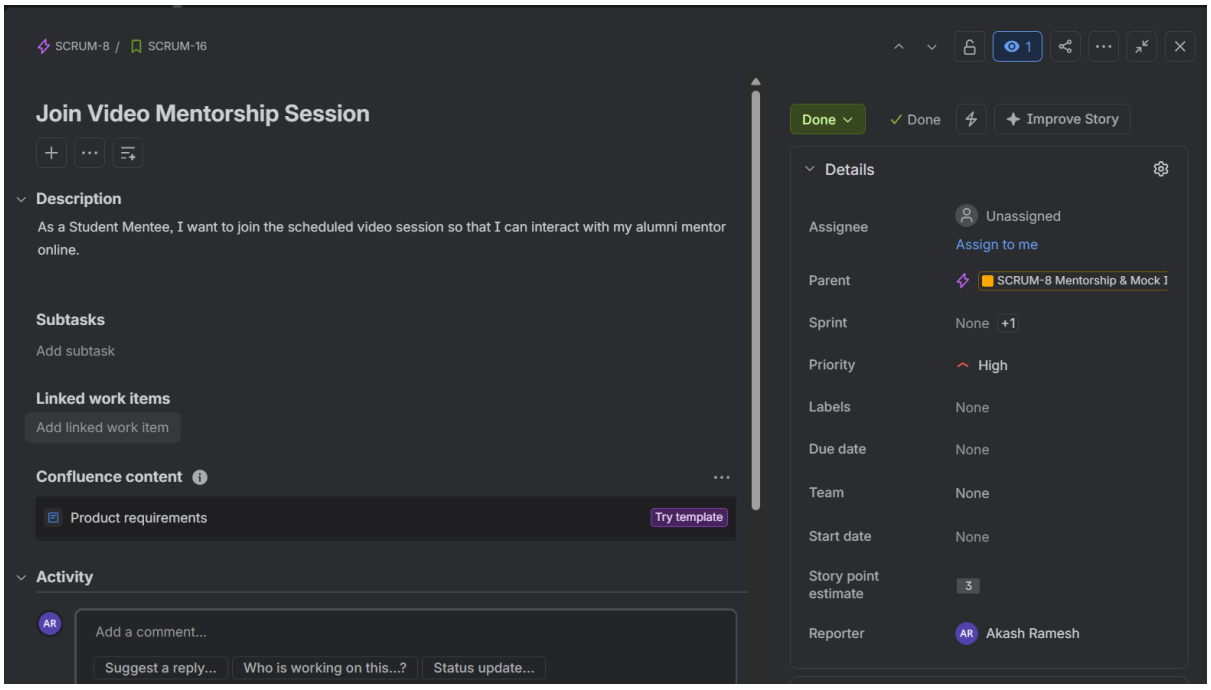

SCRUM-6 / SCRUM-11
Search Alumni Mentors
Description
As a Student Mentee, I want to search for alumni mentors based on my requirements so that I can find a suitable mentor.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Status update...
Thanks...
Done
Done
Improve Story
Details
Assignee
Akash Ramesh
Parent
SCRUM-6 Mentor Discovery & I
Sprint
None +1
Priority
High
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
3
Reporter
Akash Ramesh
Development

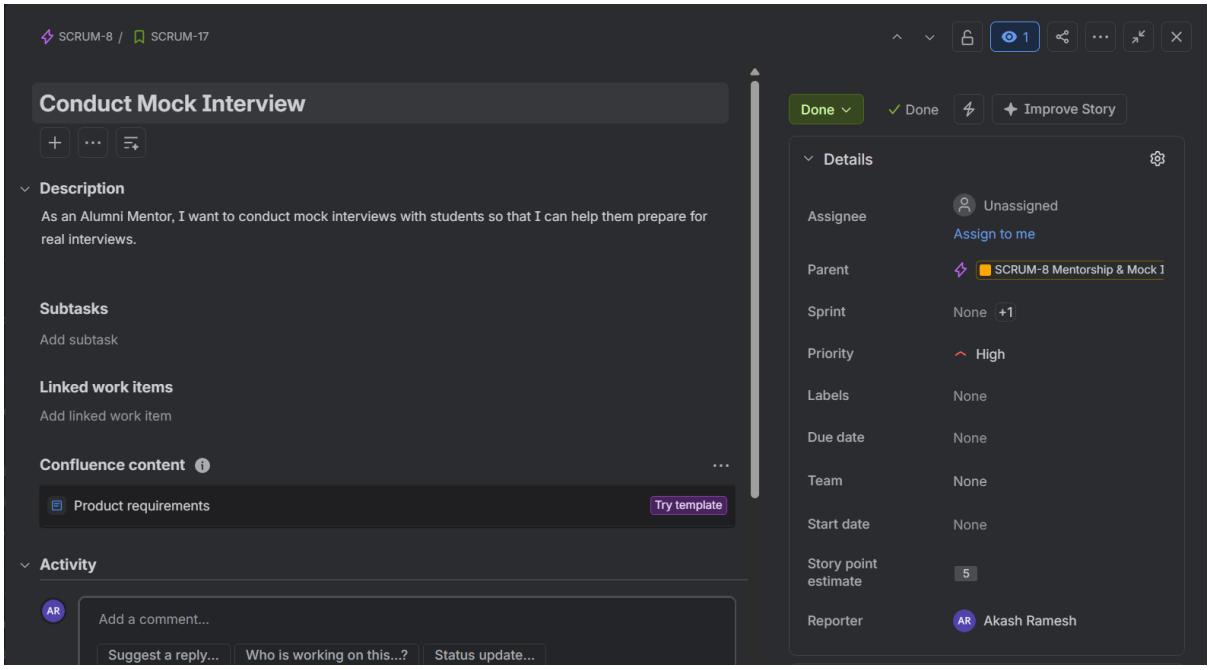

SCRUM-6 / SCRUM-12
Match Student with Mentor
Add apps
As a Student Mentee, I want the system to match me with suitable alumni mentors so that I can choose a mentor relevant to my needs.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-6 Mentor Discovery & I
Sprint
None +1
Priority
Highest
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
5
Reporter
Akash Ramesh

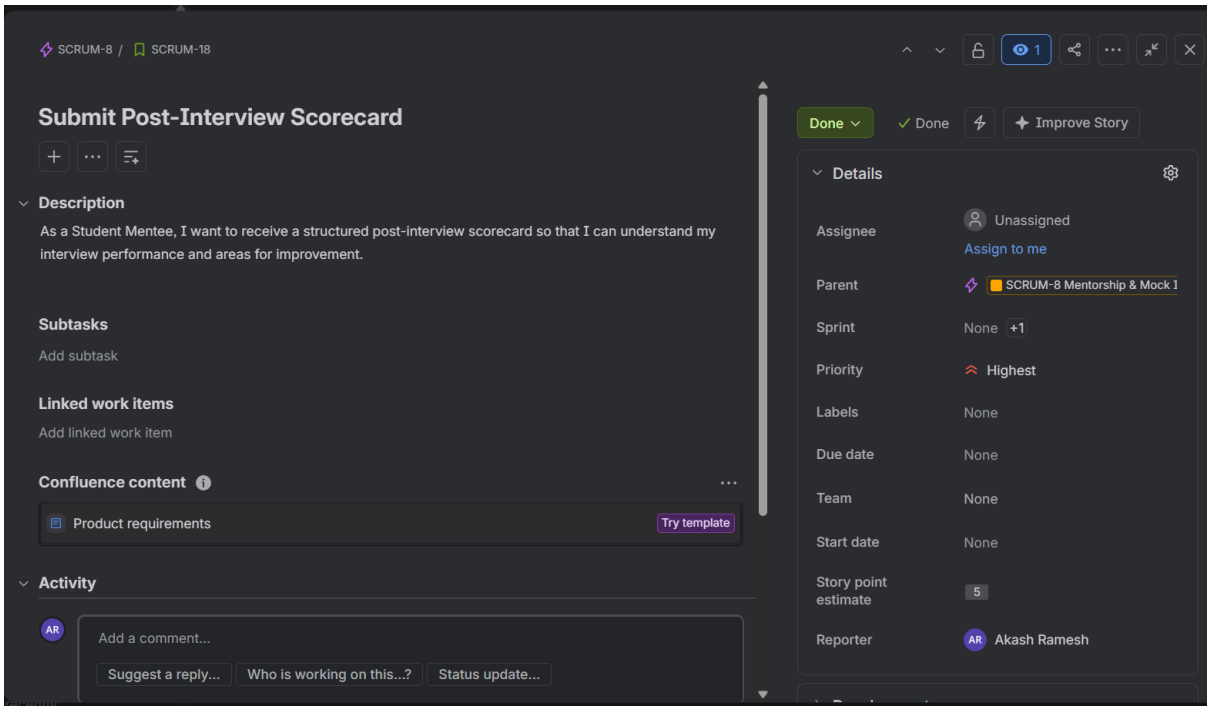

SCRUM-7 / SCRUM-13
View Mentor Availability
Description
As a Student Mentee, I want to view a mentor's available time slots so that I can select a convenient session time.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-7 Session Booking & S
Sprint
None +1
Priority
Highest
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
3
Reporter
Akash Ramesh

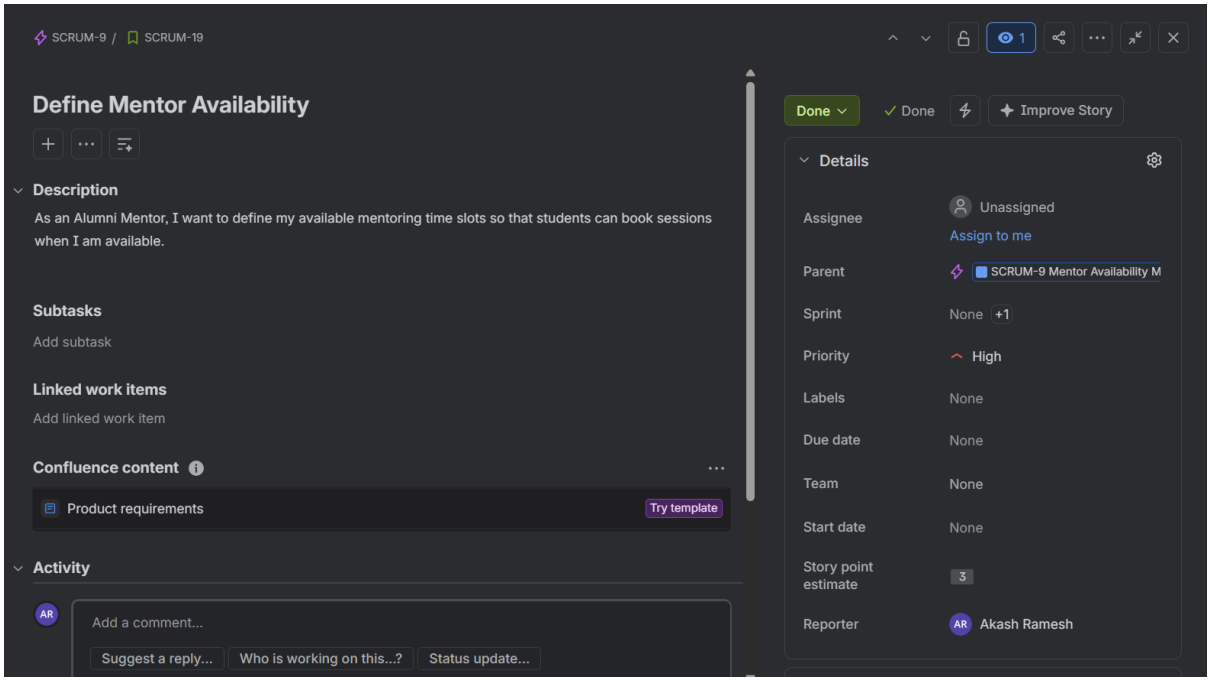

SCRUM-7 / SCRUM-14
Book Mentorship Session
Description
As a Student Mentee, I want to book an available mentorship session so that I can schedule a session with my selected mentor.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-7 Session Booking & S
Sprint
None +1
Priority
Highest
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
5
Reporter
Akash Ramesh

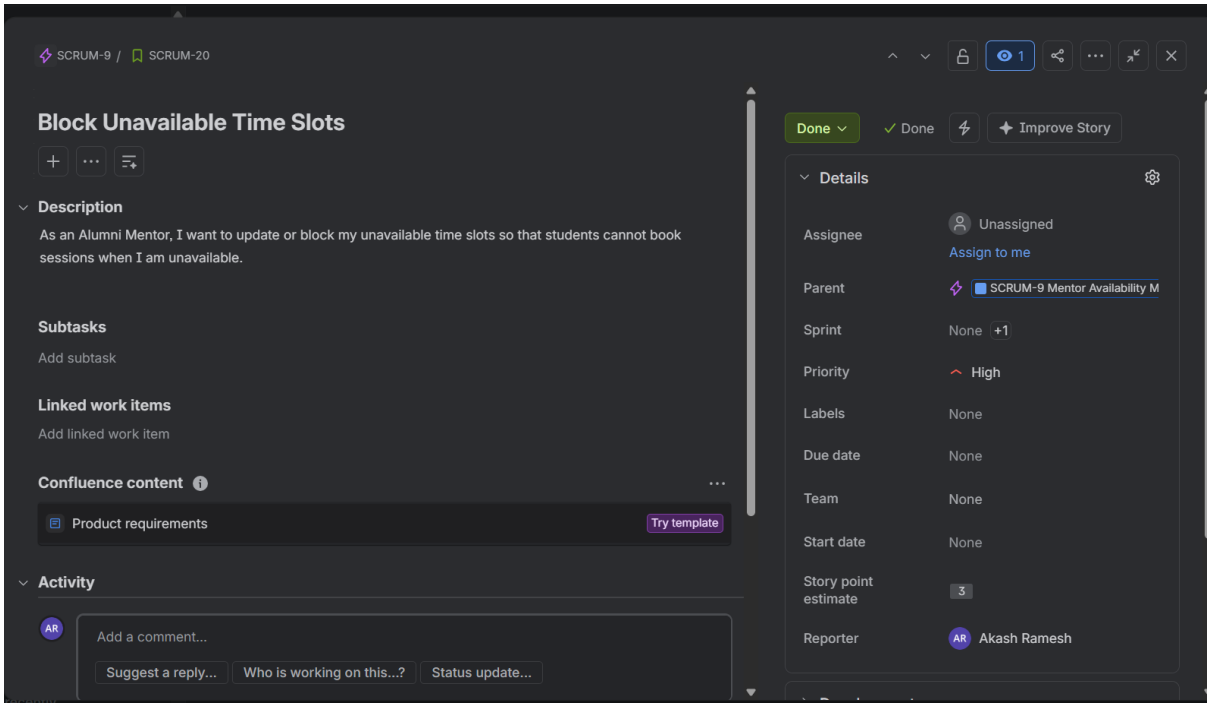

SCRUM-7 / SCRUM-15
Synchronize Session with Calendar
Description
As a Student Mentee, I want my booked session to be synchronized with the calendar so that I can keep track of my scheduled session.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-7 Session Booking & S
Sprint
None +1
Priority
High
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
3
Reporter
Akash Ramesh

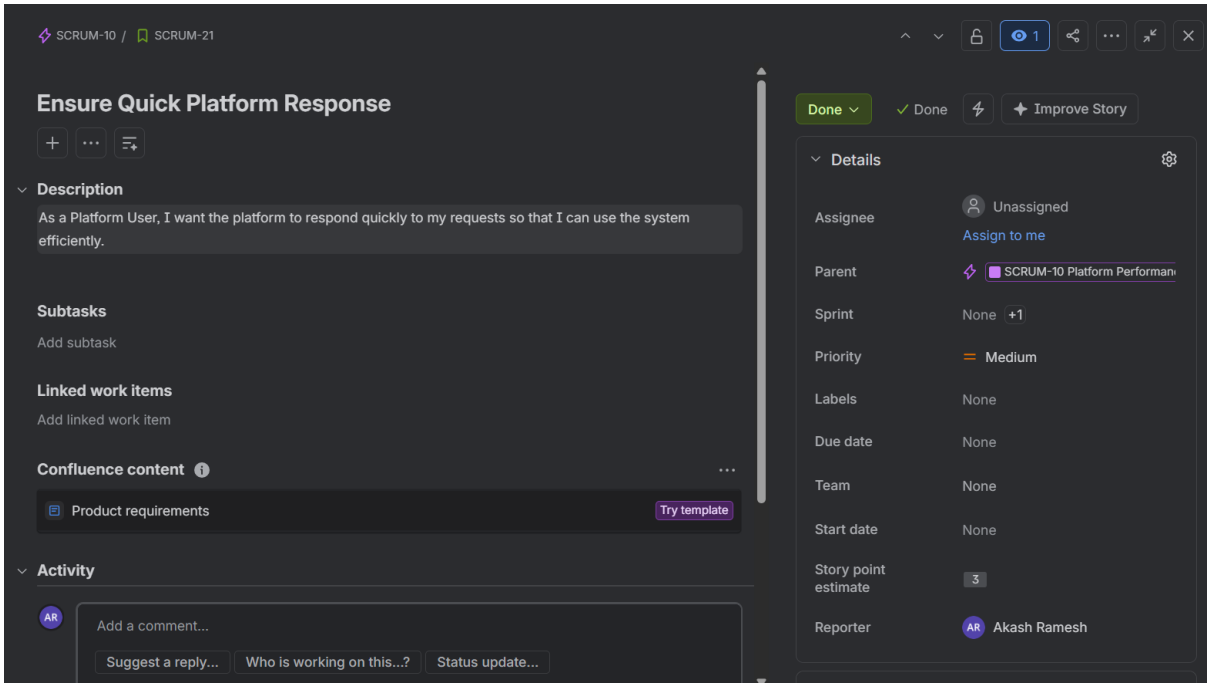

SCRUM-8 / SCRUM-16
Join Video Mentorship Session
Description
As a Student Mentee, I want to join the scheduled video session so that I can interact with my alumni mentor online.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-8 Mentorship & Mock I
Sprint
None +1
Priority
High
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
3
Reporter
Akash Ramesh

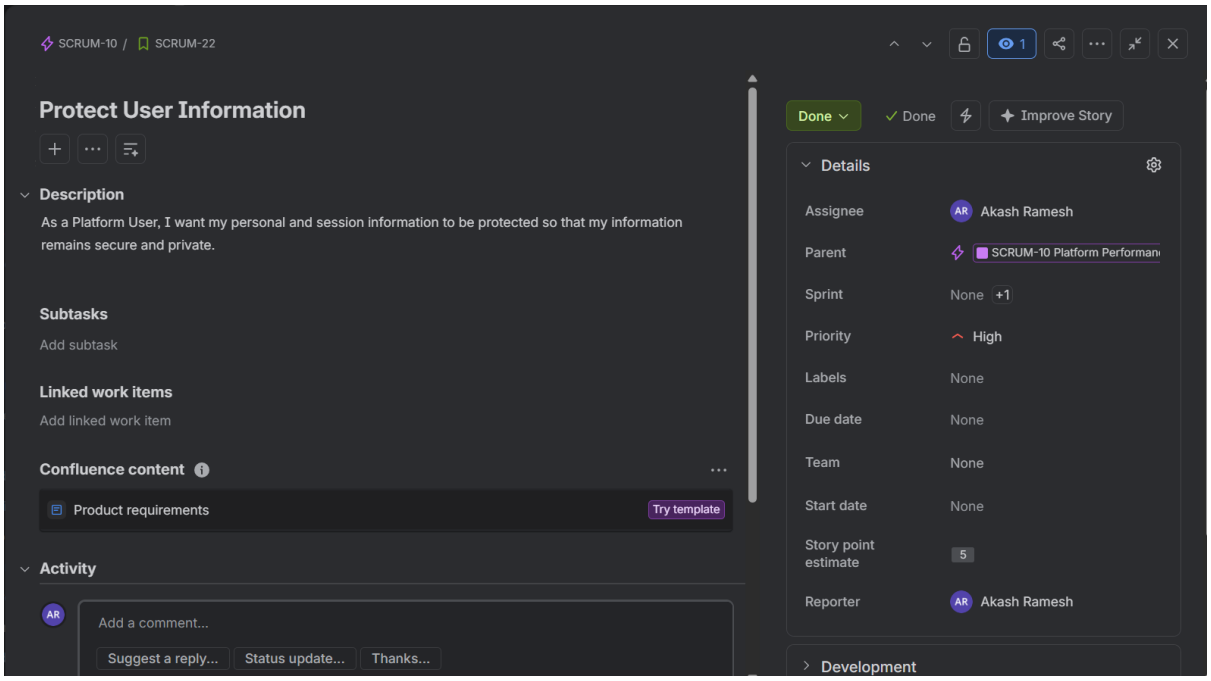

SCRUM-8 / SCRUM-17
1
Conduct Mock Interview
Done
Done
Improve Story
Description
As an Alumni Mentor, I want to conduct mock interviews with students so that I can help them prepare for real interviews.
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-8 Mentorship & Mock I
Sprint
None +1
Priority
High
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
5
Reporter
Akash Ramesh
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...


SCRUM-8 / SCRUM-18
1
Submit Post-Interview Scorecard
Done
Done
Improve Story
Description
As a Student Mentee, I want to receive a structured post-interview scorecard so that I can understand my interview performance and areas for improvement.
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-8 Mentorship & Mock I
Sprint
None +1
Priority
Highest
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
5
Reporter
Akash Ramesh
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...


SCRUM-9 / SCRUM-19
Define Mentor Availability
Description
As an Alumni Mentor, I want to define my available mentoring time slots so that students can book sessions when I am available.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-9 Mentor Availability M
Sprint
None +1
Priority
High
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
3
Reporter
Akash Ramesh


SCRUM-9 / SCRUM-20
Block Unavailable Time Slots
Description
As an Alumni Mentor, I want to update or block my unavailable time slots so that students cannot book sessions when I am unavailable.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-9 Mentor Availability M
Sprint
None +1
Priority
High
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
3
Reporter
Akash Ramesh


SCRUM-10 / SCRUM-21
Ensure Quick Platform Response
Description
As a Platform User, I want the platform to respond quickly to my requests so that I can use the system efficiently.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-10 Platform Performan
Sprint
None +1
Priority
Medium
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
3
Reporter
Akash Ramesh

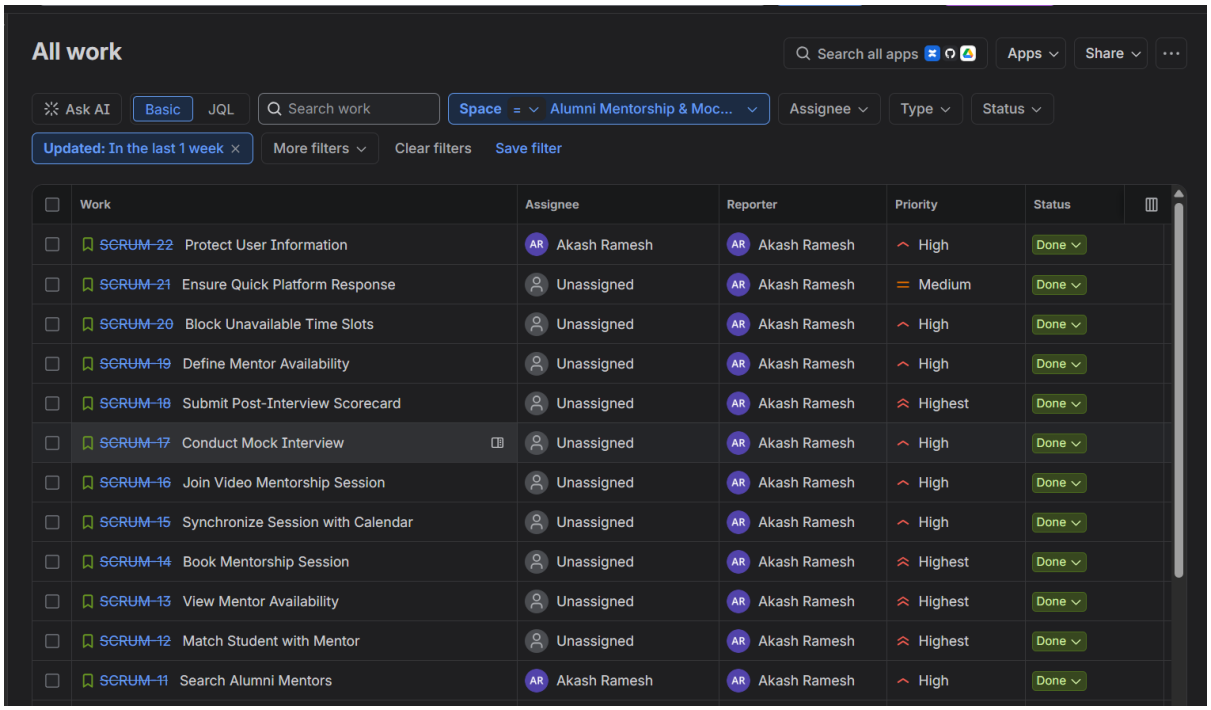

SCRUM-10 / SCRUM-22
Protect User Information
Description
As a Platform User, I want my personal and session information to be protected so that my information remains secure and private.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Status update...
Thanks...
Done
Done
Improve Story
Details
Assignee
Akash Ramesh
Parent
SCRUM-10 Platform Performan
Sprint
None +1
Priority
High
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
5
Reporter
Akash Ramesh
Development

3. Priority and Backlog Ranking

Priority was assigned to each User Story in Jira using values such as **Highest, High and Medium**.

The backlog was then arranged according to the importance of the functionality. Higher-priority stories were considered first during sprint planning.

The prioritisation helped ensure that important platform functionality such as mentor matching, session booking, mock interviews and security could be addressed early.



Work	Assignee	Reporter	Priority	Status
~~SCRUM-22~~ Protect User Information	Akash Ramesh	Akash Ramesh	High	Done
~~SCRUM-21~~ Ensure Quick Platform Response	Unassigned	Akash Ramesh	Medium	Done
~~SCRUM-20~~ Block Unavailable Time Slots	Unassigned	Akash Ramesh	High	Done
~~SCRUM-19~~ Define Mentor Availability	Unassigned	Akash Ramesh	High	Done
~~SCRUM-18~~ Submit Post-Interview Scorecard	Unassigned	Akash Ramesh	Highest	Done
~~SCRUM-17~~ Conduct Mock Interview	Unassigned	Akash Ramesh	High	Done
~~SCRUM-16~~ Join Video Mentorship Session	Unassigned	Akash Ramesh	High	Done
~~SCRUM-15~~ Synchronize Session with Calendar	Unassigned	Akash Ramesh	High	Done
~~SCRUM-14~~ Book Mentorship Session	Unassigned	Akash Ramesh	Highest	Done
~~SCRUM-13~~ View Mentor Availability	Unassigned	Akash Ramesh	Highest	Done
~~SCRUM-12~~ Match Student with Mentor	Unassigned	Akash Ramesh	Highest	Done
~~SCRUM-11~~ Search Alumni Mentors	Akash Ramesh	Akash Ramesh	High	Done

Sprint 1

Sprint 1 Planning

Sprint 1 was created to implement the core functionality required for mentor discovery, availability, session booking and basic platform security.

The following six User Stories were included in Sprint 1:

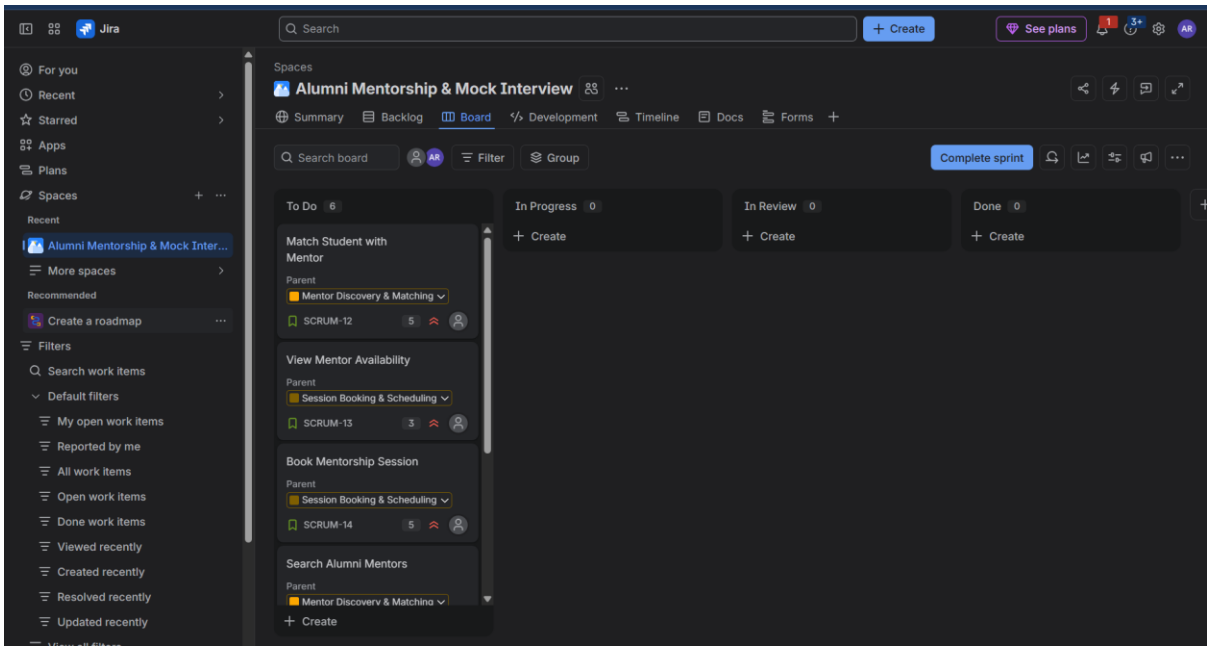
User Story	Story Points
Match Student with Mentor	5
View Mentor Availability	3
Book Mentorship Session	5
Search Alumni Mentors	3
Define Mentor Availability	3
Protect User Information	5
Total	**24**

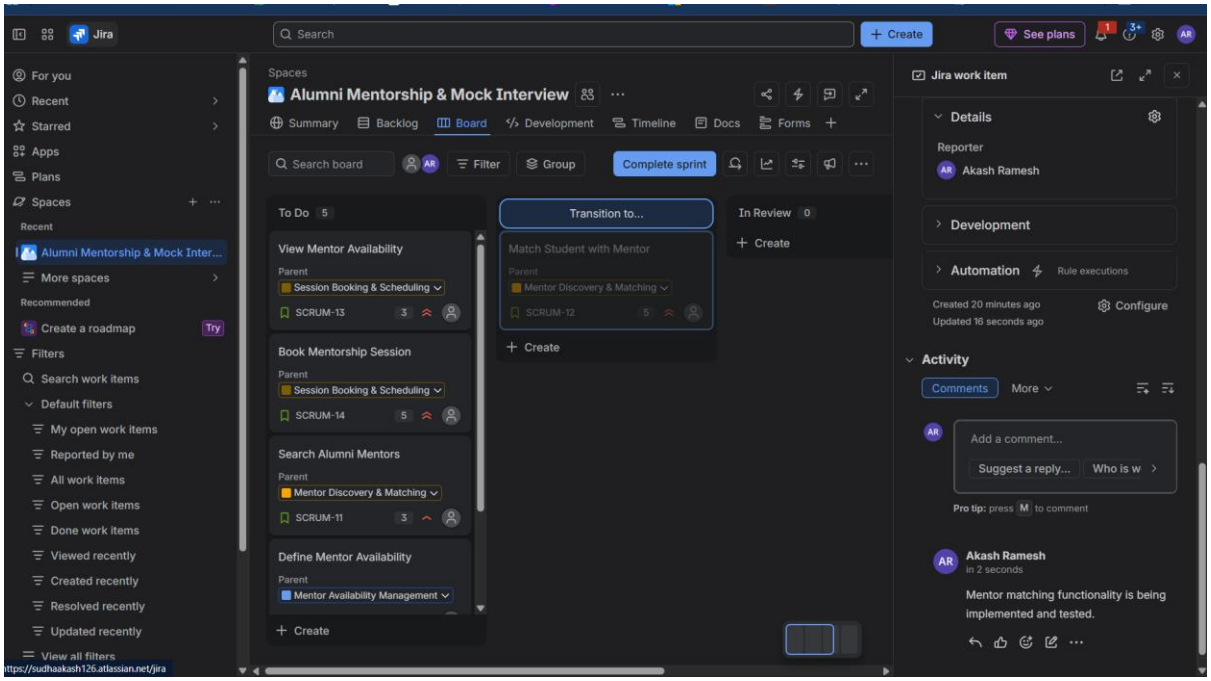
Sprint Goal

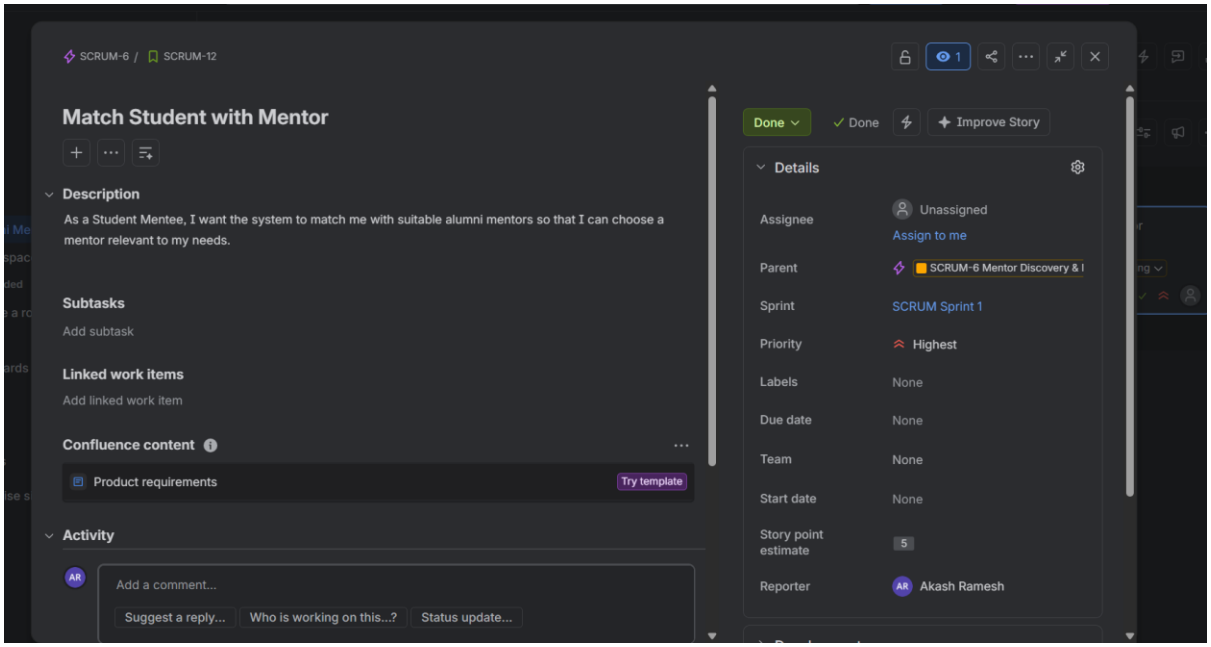
Implement the core mentor discovery, availability, booking, and basic security functionality.

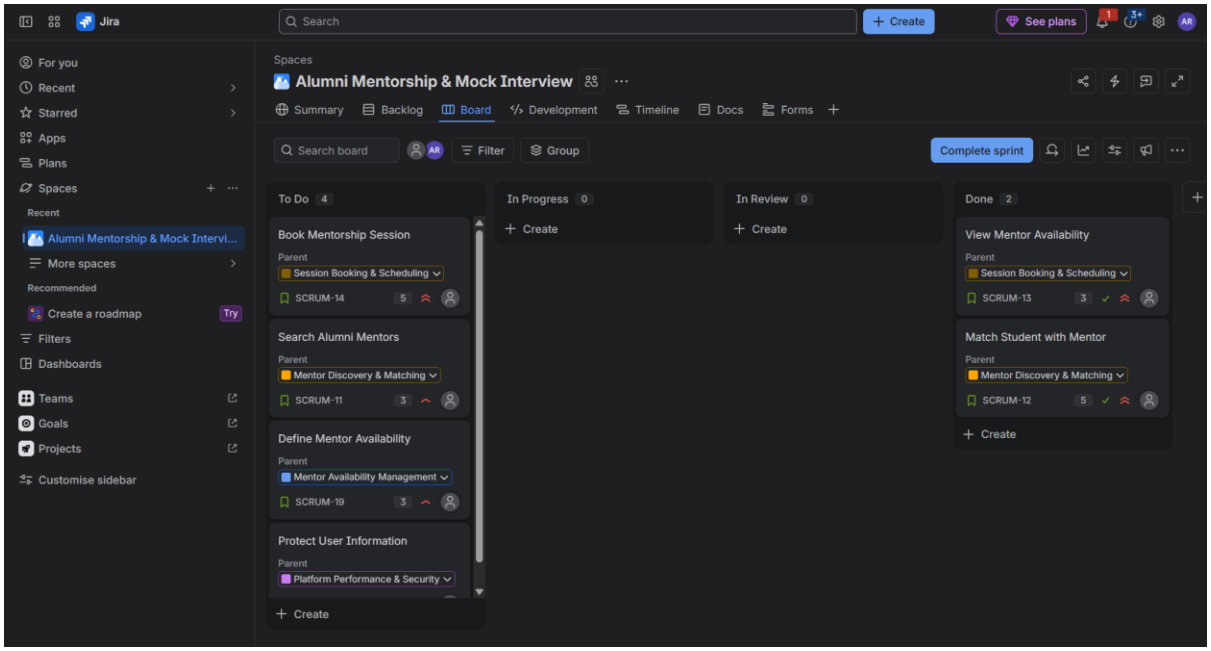
Sprint 1 Progress and Comments

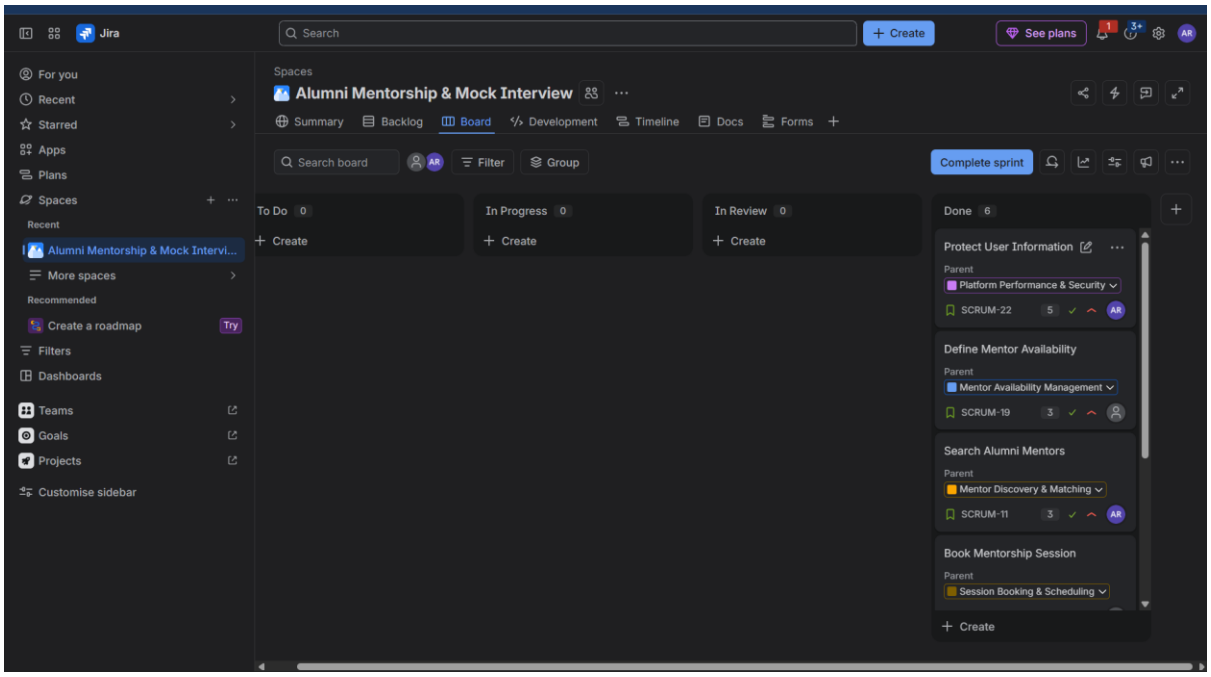
Sprint progress was simulated by moving the User Stories through the Jira workflow from **To Do → In Progress → Done** and adding comments to indicate progress.




Jira
Search
Create
See plans
For you
Recent
Starred
Apps
Plans
Spaces
Recent
Alumni Mentorship & Mock Inter...
More spaces
Recommended
Create a roadmap
Try
Filters
Search work items
Default filters
My open work items
Reported by me
All work items
Open work items
Done work items
Viewed recently
Created recently
Resolved recently
Updated recently
View all filters
Spaces
Alumni Mentorship & Mock Interview
Summary
Backlog
Board
Development
Timeline
Docs
Forms
Search board
Filter
Group
Complete sprint
To Do 5
View Mentor Availability
Parent
Session Booking & Scheduling
SCRUM-13
Book Mentorship Session
Parent
Session Booking & Scheduling
SCRUM-14
Search Alumni Mentors
Parent
Mentor Discovery & Matching
SCRUM-11
Define Mentor Availability
Parent
Mentor Availability Management
Create
Transition to...
Match Student with Mentor
Parent
Mentor Discovery & Matching
SCRUM-12
Create
In Review 0
Create
Jira work item
Details
Reporter
Akash Ramesh
Development
Automation
Rule executions
Created 20 minutes ago
Updated 16 seconds ago
Configure
Activity
Comments
More
Add a comment...
Suggest a reply...
Who is w
Pro tip: press M to comment
Akash Ramesh
in 2 seconds
Mentor matching functionality is being implemented and tested.
https://sudhaakash126.atlassian.net/jira


SCRUM-6 / SCRUM-12
Match Student with Mentor
Description
As a Student Mentee, I want the system to match me with suitable alumni mentors so that I can choose a mentor relevant to my needs.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template
Activity
Add a comment...
Suggest a reply...
Who is working on this...?
Status update...
Done
Done
Improve Story
Details
Assignee
Unassigned
Assign to me
Parent
SCRUM-6 Mentor Discovery & I
Sprint
SCRUM Sprint 1
Priority
Highest
Labels
None
Due date
None
Team
None
Start date
None
Story point estimate
5
Reporter
Akash Ramesh

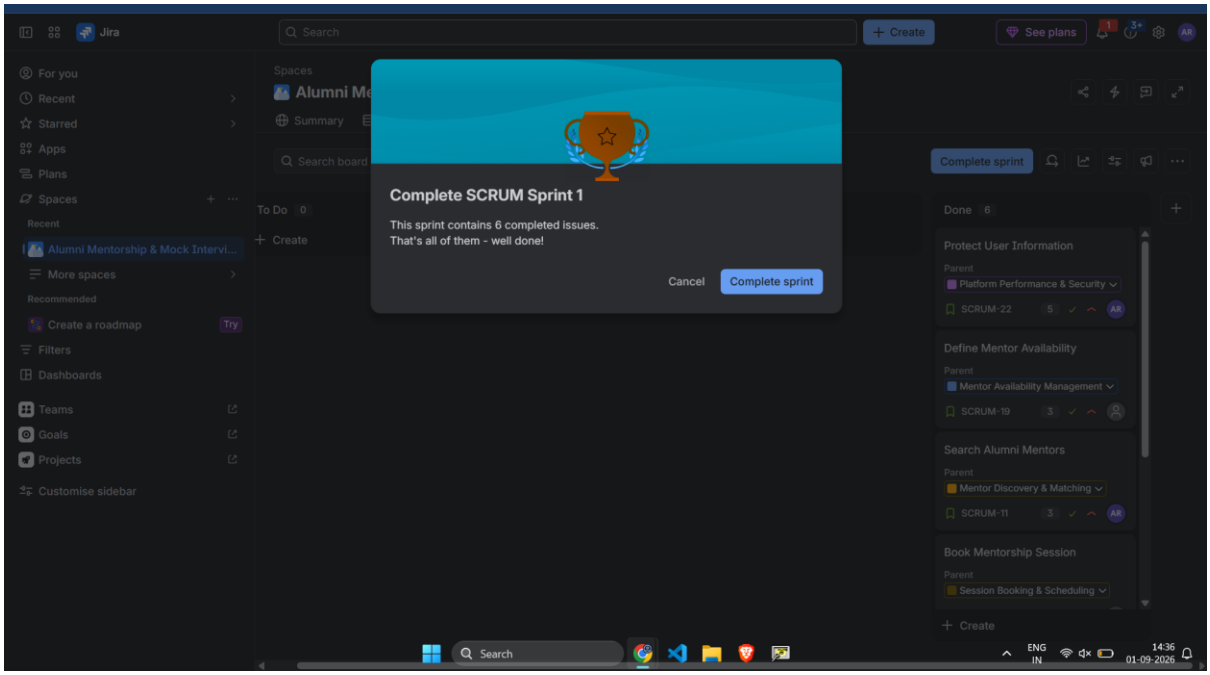




Sprint 1 Completion

At the end of Sprint 1, all six committed User Stories were moved to the **Done** column.

The completed stories represented a total of **24 story points**.



Sprint 2

After Sprint 1, the next set of User Stories was taken into Sprint 2.

Sprint 2 focused on extending the platform with calendar synchronization, video mentorship, mock interviews, post-interview feedback, availability controls and performance.

The following six User Stories were included in Sprint 2:

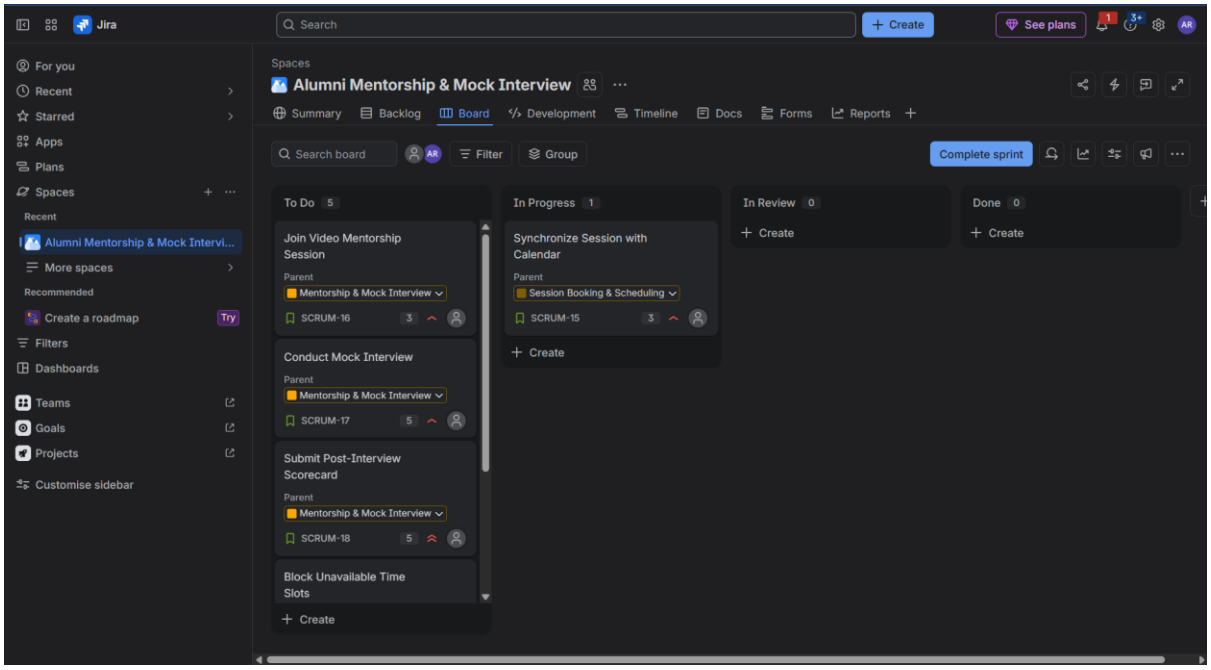
User Story	Story Points
Synchronize Session with Calendar	3
Join Video Mentorship Session	3
Conduct Mock Interview	5
Submit Post-Interview Scorecard	5
Block Unavailable Time Slots	3

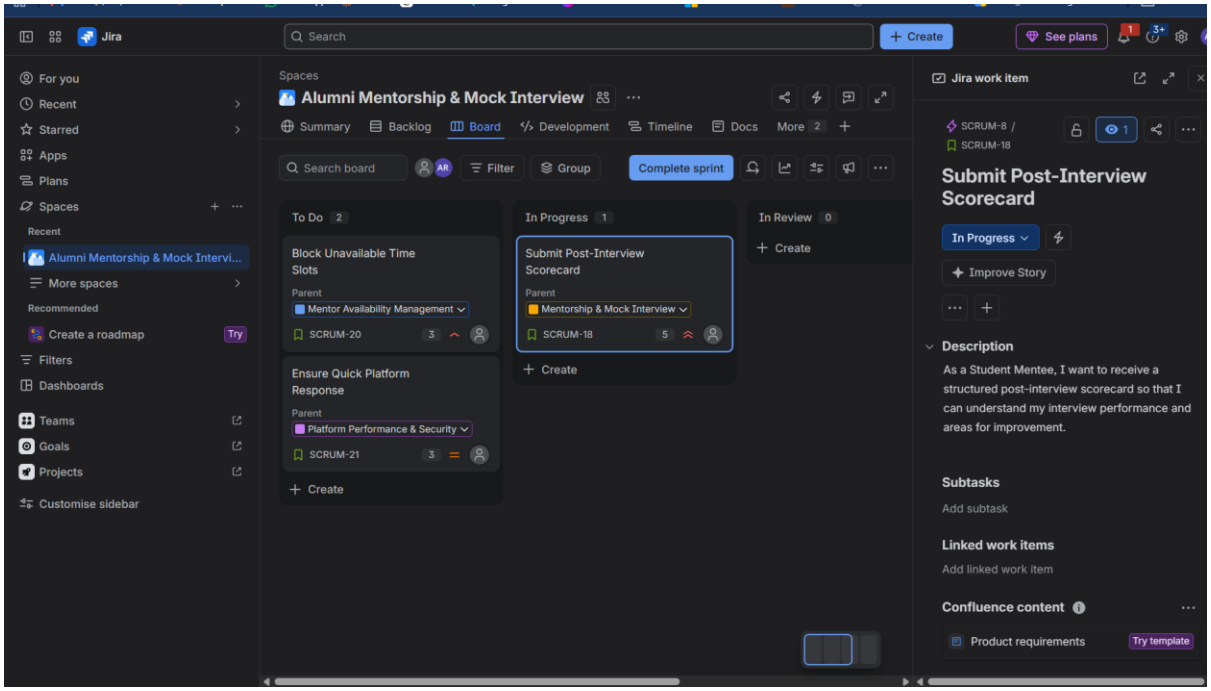
Ensure Quick Platform Response	3
Total	**22**

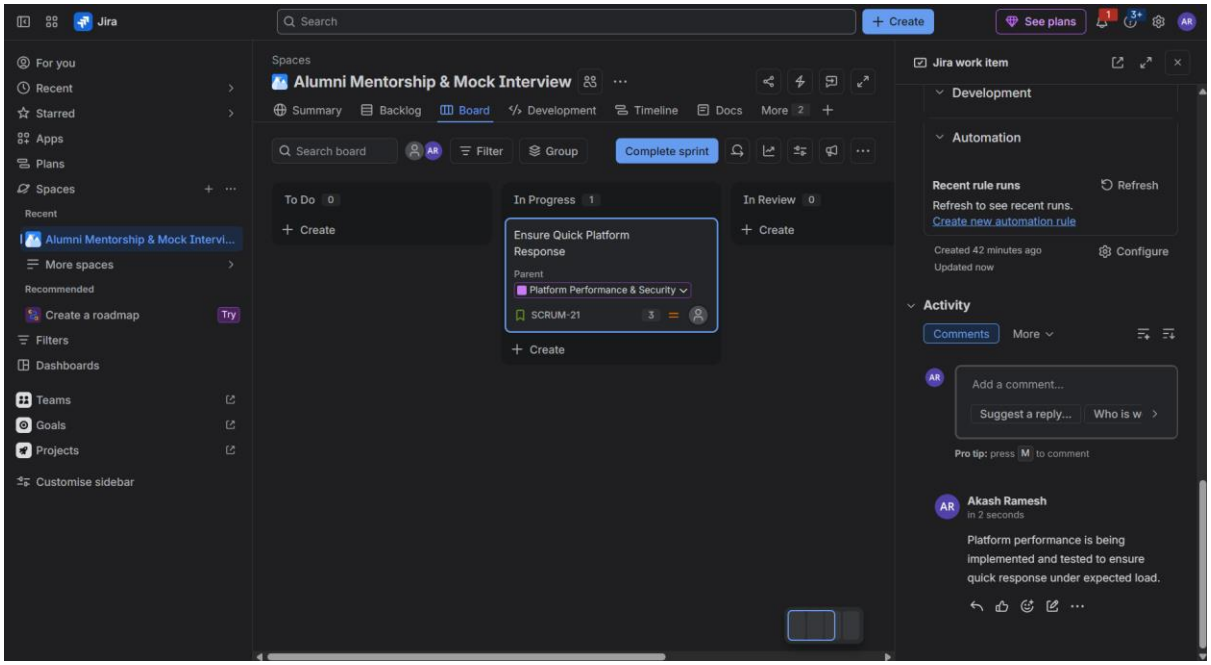
Sprint Goal
Complete mentorship, mock interview, feedback, calendar, and performance functionality.

Sprint 2 Progress and Comments

Sprint 2 followed the same workflow used in Sprint 1. User Stories were moved from To Do to In Progress and finally to Done, with progress comments recorded in Jira.


Jira
Search
Create
See plans
For you
Recent
Starred
Apps
Plans
Spaces
Recent
Alumni Mentorship & Mock Intervi...
More spaces
Recommended
Create a roadmap
Try
Filters
Dashboards
Teams
Goals
Projects
Customise sidebar
Spaces
Alumni Mentorship & Mock Interview
Summary
Backlog
Board
Development
Timeline
Docs
Forms
Reports
Search board
Filter
Group
Complete sprint
To Do 5
Join Video Mentorship Session
Parent
Mentorship & Mock Interview
SCRUM-16
Conduct Mock Interview
Parent
Mentorship & Mock Interview
SCRUM-17
Submit Post-Interview Scorecard
Parent
Mentorship & Mock Interview
SCRUM-18
Block Unavailable Time Slots
Create
In Progress 1
Synchronize Session with Calendar
Parent
Session Booking & Scheduling
SCRUM-15
Create
In Review 0
Create
Done 0
Create

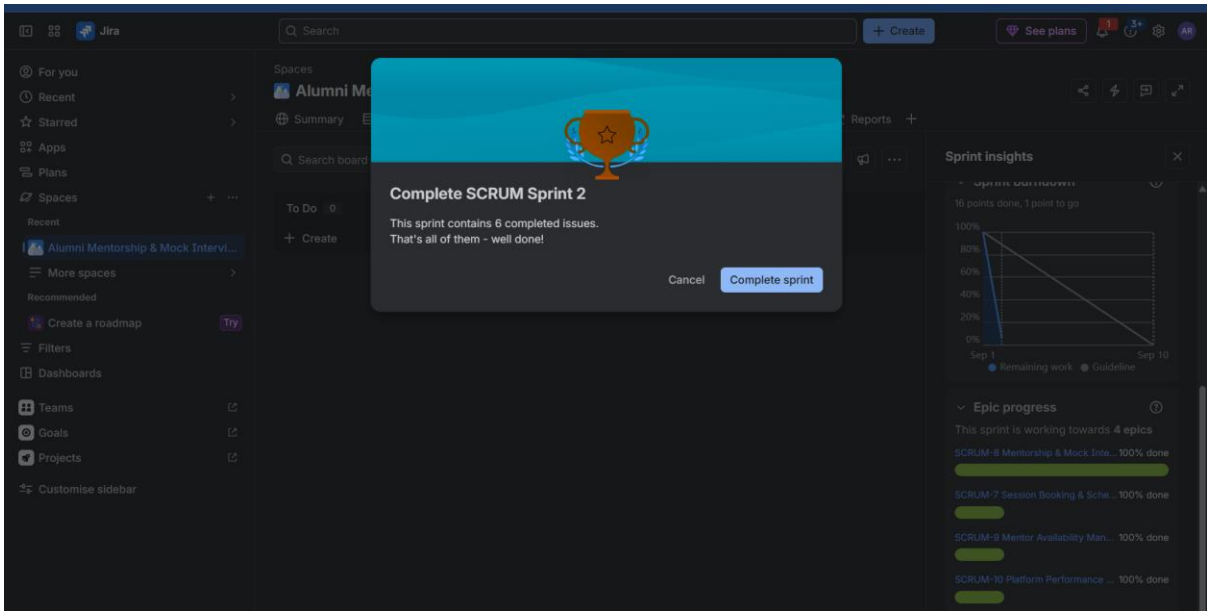

Jira
Search
Create
See plans
For you
Recent
Starred
Apps
Plans
Spaces
Recent
Alumni Mentorship & Mock Intervi...
More spaces
Recommended
Create a roadmap
Try
Filters
Dashboards
Teams
Goals
Projects
Customise sidebar
Spaces
Alumni Mentorship & Mock Interview
Summary
Backlog
Board
Development
Timeline
Docs
More 2
Search board
Filter
Group
Complete sprint
To Do 2
Block Unavailable Time Slots
Parent
Mentor Availability Management
SCRUM-20
Ensure Quick Platform Response
Parent
Platform Performance & Security
SCRUM-21
Create
In Progress 1
Submit Post-Interview Scorecard
Parent
Mentorship & Mock Interview
SCRUM-18
Create
In Review 0
Create
Jira work item
SCRUM-8 / SCRUM-18
Submit Post-Interview Scorecard
In Progress
Improve Story
Description
As a Student Mentee, I want to receive a structured post-interview scorecard so that I can understand my interview performance and areas for improvement.
Subtasks
Add subtask
Linked work items
Add linked work item
Confluence content
Product requirements
Try template



Sprint 2 Completion

At the end of Sprint 2, all six committed User Stories were moved to the **Done** column.

The completed stories represented **22 story points**.



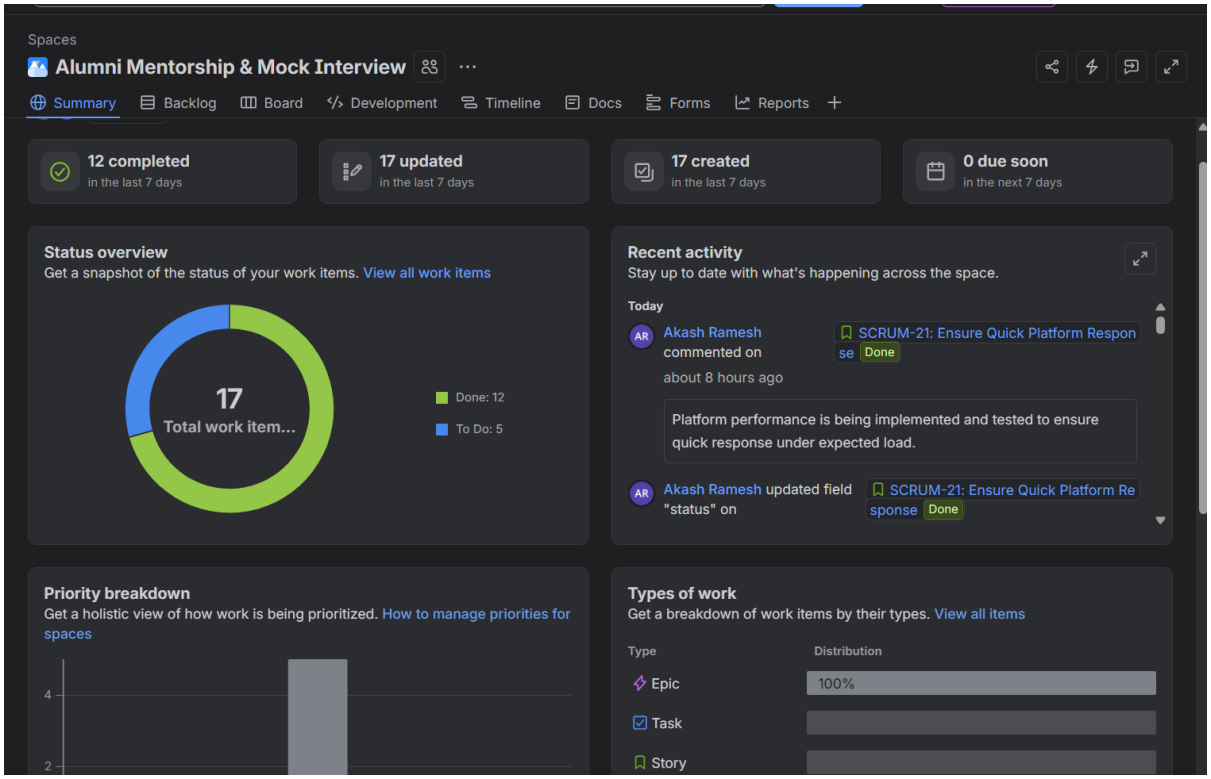
Sprint Summary

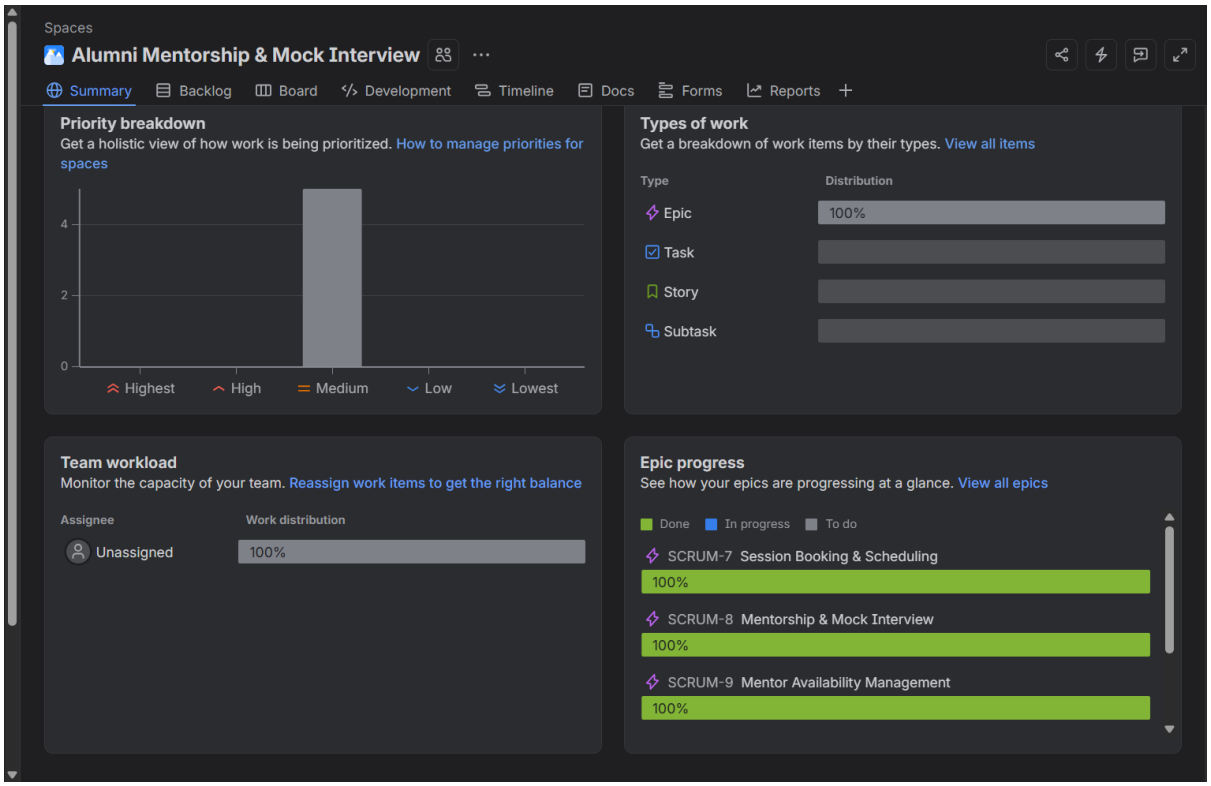
Sprint 1 Summary

Sprint 1 focused on the core mentor discovery, availability, booking and security functionality.

The six committed User Stories were completed successfully, representing **24 story points**.

Sprint 2 extended the platform with calendar integration, video mentorship, mock interview, scorecard, availability and performance functionality. The six committed User Stories were completed successfully, representing **22 story points**.



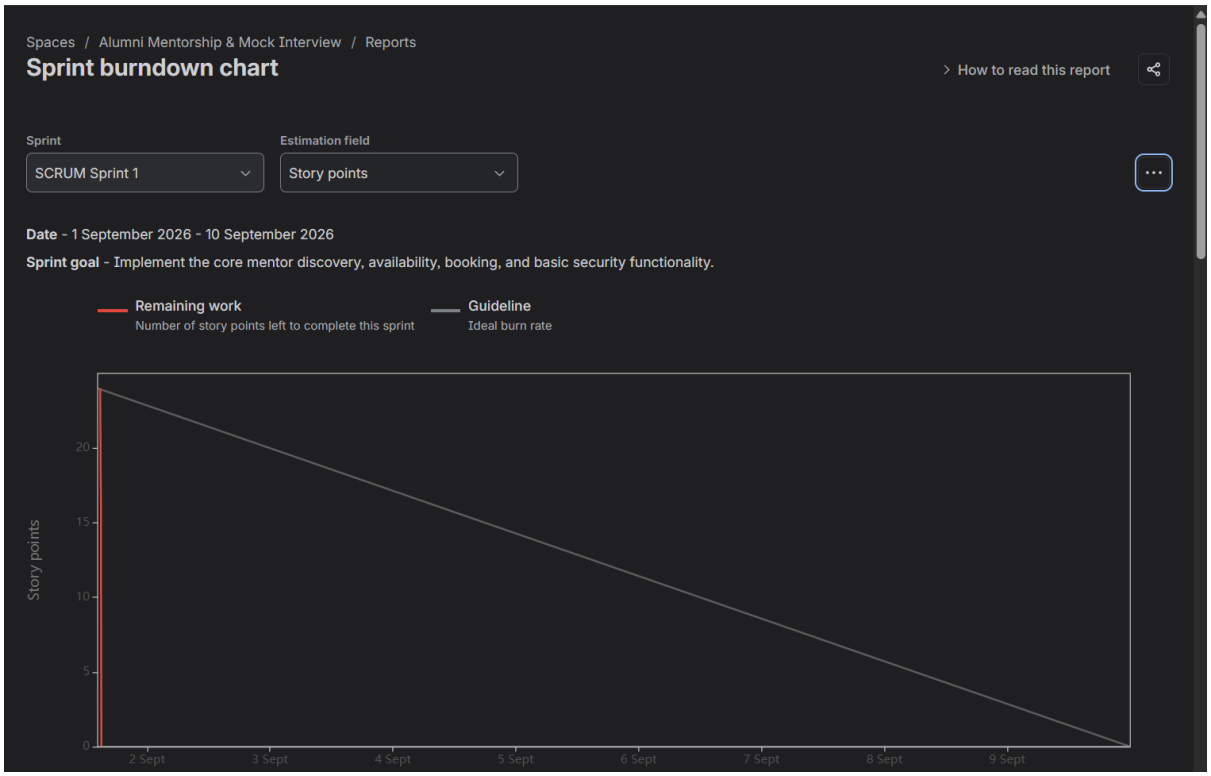


Burndown Chart

The Jira Burndown Chart shows the amount of remaining work in story points during the sprint. The chart compares the remaining work against the ideal guideline.

Sprint 1 Burndown Chart

Sprint 1 started with **24 story points** and reached **0 remaining story points** after the committed User Stories were completed.



Sprint 2 Burndown Chart

Sprint 2 started with **22 story points** and reached **0 remaining story points** after completion of the committed User Stories.

Sprint insights

Learn more

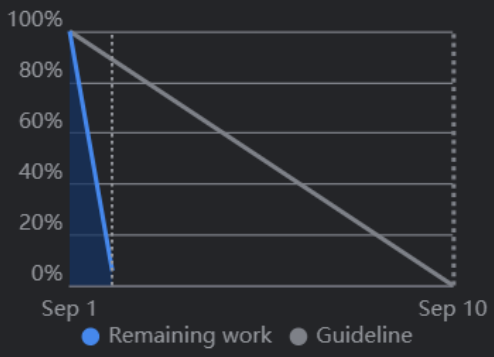
Sprint progress

100% done

Done	In progress	Not started
100%	0%	0%

Sprint burndown

16 points done, 1 point to go

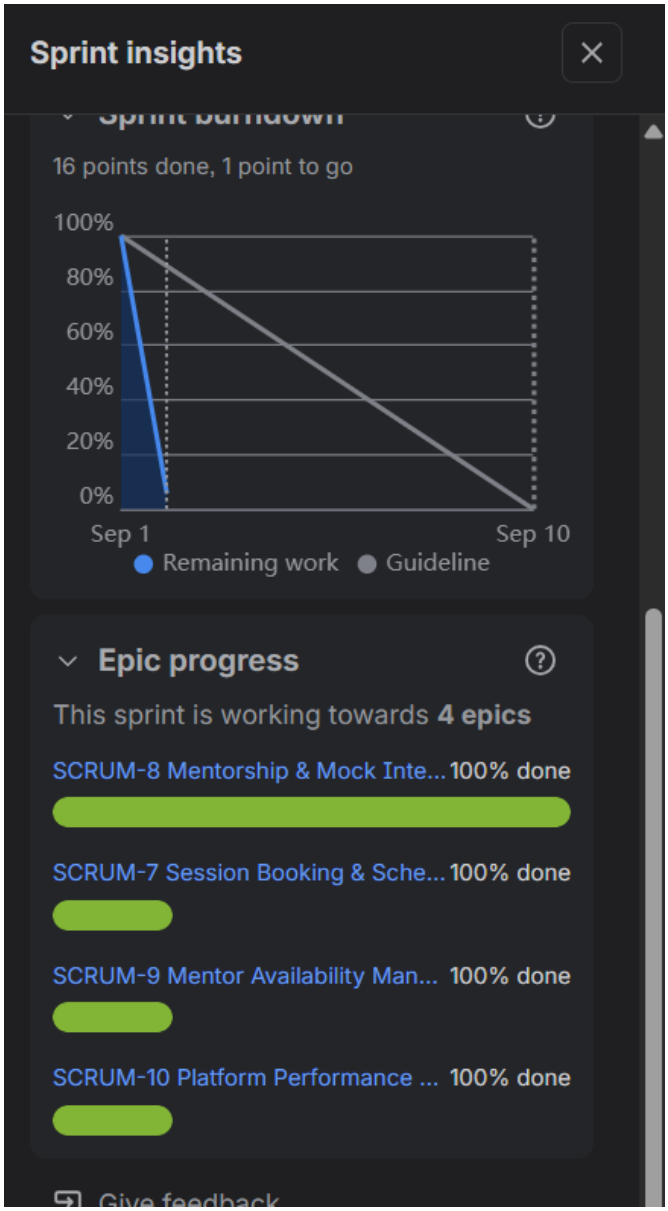


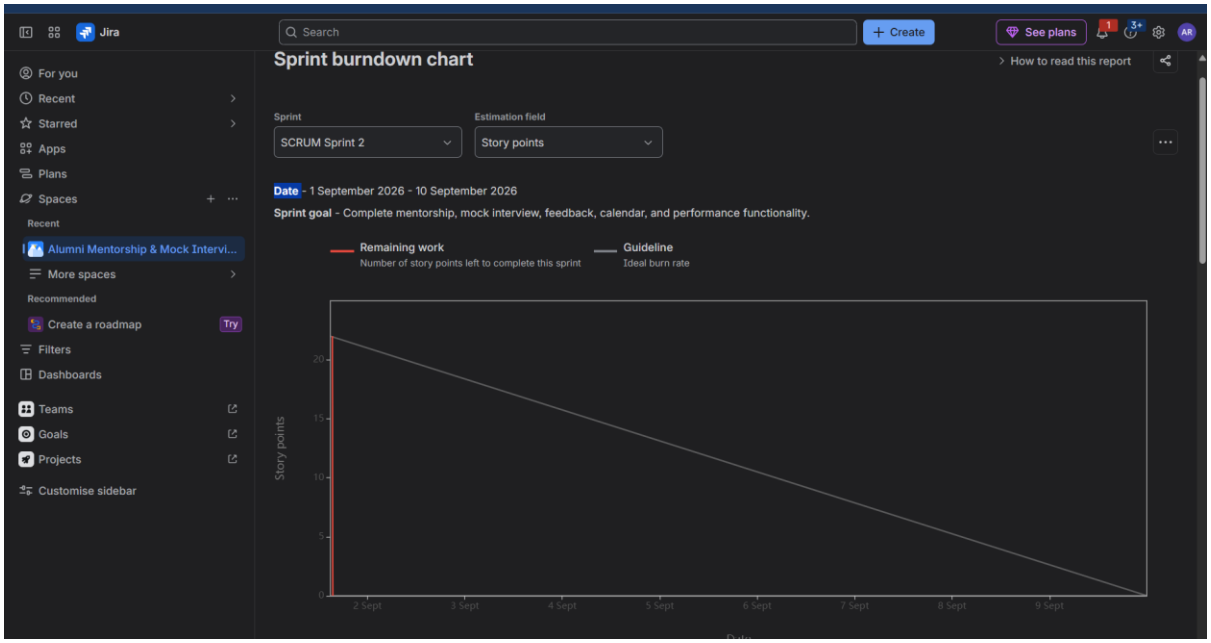
Epic progress

This sprint is working towards **4 epics**

SCRUM-8 Mentorship & Mock Inte... 100% done

SCRUM-7 Session Booking & Sche... 100% done


Sprint insights
16 points done, 1 point to go
100%
80%
60%
40%
20%
0%
Sep 1
Sep 10
Remaining work
Guideline
Epic progress
This sprint is working towards 4 epics
SCRUM-8 Mentorship & Mock Inte... 100% done
SCRUM-7 Session Booking & Sche... 100% done
SCRUM-9 Mentor Availability Man... 100% done
SCRUM-10 Platform Performance ... 100% done
Give feedback



Reflection

What I Learned from Using Jira

Creating the Alumni Mentorship & Mock Interview Platform as a collection of Epics and User Stories helped me understand how a software project can be divided into smaller and manageable pieces of work.

The Epic structure provided a clear separation between major areas of the platform, while the User Stories described specific functionality from the perspective of the users.

Planning Poker and Story Point Estimation

Using story points helped estimate the relative complexity of the User Stories instead of assigning estimates only in terms of hours.

The Fibonacci-based values of 3 and 5 were used to represent different levels of complexity. Larger stories required more effort and consideration during sprint planning.

Backlog Prioritisation

Assigning priorities helped identify which functionality should be implemented first.

Features such as mentor matching, session booking, mock interviews and security were treated as important parts of the platform. Ranking the backlog made sprint planning easier because the higher-priority functionality could be selected first.

Sprint Planning and Progress Tracking

Sprint 1 concentrated on the core functionality of mentor discovery, availability, booking and security. Sprint 2 extended the system with calendar synchronization, video mentorship, mock interviews, feedback and performance-related functionality.

Moving User Stories through **To Do, In Progress and Done** provided a visible representation of sprint progress. Comments added to the Jira issues also provided a record of the work being performed.

What Went Well

The project was successfully divided into five Epics and twelve User Stories. All User Stories selected for Sprint 1 and Sprint 2 were completed during the Jira simulation.

The use of story points, priorities and sprint organisation made the backlog easier to understand and helped maintain a structured workflow.

What Was Challenging

One challenge was estimating the complexity of the different User Stories. Features such as mentor matching, booking, mock interviews and scorecards involve multiple activities and therefore required careful consideration when assigning story points.

Another challenge was maintaining a realistic sprint workflow while simulating development activity within Jira.

What Could Be Improved

In a real development project, progress would be recorded throughout the sprint rather than completing all the work during a single simulation session.

The User Stories could also be assigned to specific team members, and acceptance criteria could be defined more explicitly so that every completed story can be independently verified.

Future sprints could also break larger stories into smaller tasks to make progress easier to track and to produce a more gradual burndown.

Conclusion

The Alumni Mentorship & Mock Interview Platform was successfully modelled and planned using Jira and Agile Scrum practices.

The project was divided into five Epics and twelve User Stories. Story points and priorities were assigned to the User Stories, after which the backlog was organised into two sprints.

Sprint 1 focused on the core mentor discovery, availability, booking and security functionality, while Sprint 2 focused on calendar integration, video mentorship, mock interviews, feedback, availability controls and platform performance.

The sprint boards, comments, summaries and Burndown Charts provided evidence of the Agile workflow and progress tracking performed during the project.
